



## Manatee Bay Elementary School

19200 SW 36 STREET, WESTON 33332

Location Num	3841
Board District	6
Board Member	Laurie Rich Levinson
ADEFP Budget*	\$3,093,861
Total Facilities Budget	\$2,484,661

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.


- All dates are based on calendar year. SMART funded projects are included.
- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

### PRIMARY PROJECTS CURRENT STATUS: Complete

Primary Renovation: Complete.

School Choice Enhancements: COMPLETED 04/2018 - Voting completed 6/10/16. (2) 6' benches with copies, computers, carts, robotics material, two-way radios, printers, storage shelving delivered and installed between 09/2016 and 11/2016. Media production system delivered 08/2017. Shade structure for the playground permitted on 6/2017, construction completed 11/2017. Media production upgrade delivered 08/2017. Classroom tables delivered 04/2018.

### SMART Facilities Update By Project

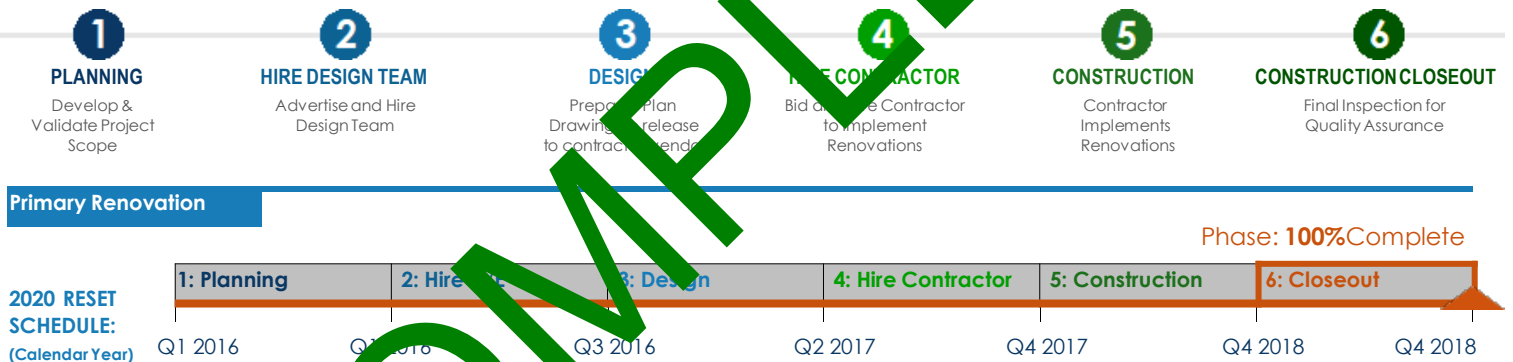

SCOPE:	BUDGET:	FLAG:
Additional Funding - Board Approved 10/17/14 (11-14)	\$625,661	COMMENTS:
Art Room Renovation and Equipment	\$65,000	
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$862,000	
Conversion of Existing Space to Music and/or Art Lab(s)	\$339,000	
HVAC Improvements	\$357,000	
Music Room Renovation	\$136,000	

## Manatee Bay Elementary School

### SMART Facilities Update by Project Cont.

#### School Choice Enhancements\*

 Phase: **100%** Complete

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete	
Planned	Q1 2016	Q2 2016	Q4 2017	Q4 2017
Actual	01/2016	06/2016	04/2018	04/2018
<b>SCOPE:</b>	<b>BUDGET:</b>		<b>FLAG:</b>	
School Choice Enhancement	\$100,000		<b>COMMENTS:</b> <div style="border: 1px solid black; height: 30px;"></div>	

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.
