



## The Quest Center

6401 CHARLESTON STREET, HOLLYWOOD 33024

Location Num	1021
Board District	1
Board Member	Ann Murray
ADEFP Budget*	\$1,914,000
Total Facilities Budget	\$1,788,000

**\*NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included.


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

## PRIMARY PROJECTS CURRENT STATUS: **Construction**


Primary Renovation: Construction is in progress. Fire alarm and electrical improvements are in progress. A change order approval is pending for the fire alarm design. A review of the revised roofing submittals is pending.

School Choice Enhancements: Voting completed 12/8/16. Sensory room equipment delivered 09/2017. Entertainment room renovation complete 08/2018. TVs installed 09/2018.

## SMART Facilities Update By Project



### Primary Renovation

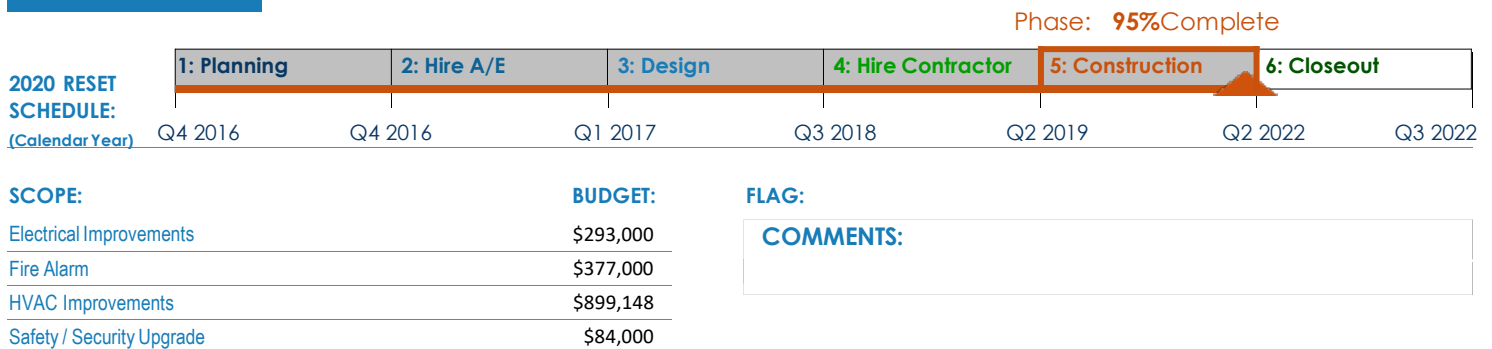

### CU Replacement



# The Quest Center

## SMART Facilities Update by Project Cont.

### RTU Replacement

 Phase: **100%** Complete

<b>2020 RESET SCHEDULE:</b> (Calendar Year)	<b>1: Planning</b>	<b>2: Hire A/E</b>	<b>3: Design</b>	<b>4: Hire Contractor</b>	<b>5: Construction</b>	<b>6: Closeout</b>
	N/A	N/A	N/A	N/A	N/A	N/A

**SCOPE:** HVAC Improvements - RTU Replacement  
**BUDGET:** \$18,327

**FLAG:**  
**COMMENTS:**

### School Choice Enhancements\*

 Phase: **84%** Complete

<b>SCHEDULE:</b>	<b>PH:1 Planning/Design</b>	<b>PH:2 Implement</b>	<b>PH:3 Complete</b>
Planned	Q1 2015	Q4 2016	TBD
Actual	11/2015	12/2016	TBD

**SCOPE:** School Choice Enhancement  
**BUDGET:** \$100,000

**FLAG:**  
**COMMENTS:**  
 Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.

\*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.
