



MUNICIPAL REPORT

For The Quarter Ending
September 30, 2020 | FY21-Q1



Established 1915

BROWARD
County Public Schools

PREFACE

We are pleased to present the updated Broward County Public Schools (BCPS) **School Spotlight** editions specifically designed for city administrators, city commissioners, council-representatives and Broward County School Board Members.

The School Spotlight is a quarterly report that details the progress of facilities projects at each of the 232 schools participating in the SMART Bond Program. This “City Edition” of The School Spotlight provides a municipal breakdown of all approved renovation projects, projected costs, School Choice Enhancement Program initiatives and other ongoing or scheduled SMART Program projects.

These easy-to-read School Spotlights allow board members and city officials to better follow the progress of the facilities improvements within specific municipalities. The Spotlights will be updated every quarter to help city officials and school board members share timely information with business groups, community organizations, homeowners’ associations and other key constituents as ongoing SMART Program projects continue to progress.

SMART (**S**afety, **M**usic & **A**rt, **A**thletics, **R**enovation and **T**echnology) is the **\$800 million capital improvement** program to upgrade existing school facilities and to purchase new computer technology, athletic equipment and musical instruments to enhance the learning experience of Broward County students.



Atlantic Technical College & Technical High School

4700 COCONUT CREEK PARKWAY, COCONUT CREEK 33063

Location Num	2221
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$10,340,400
Total Facilities Budget	\$9,052,000


***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.
 - All dates are based on calendar year. SMART funded projects are included. Only
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in permit review. Building Department currently reviewing the first submission.

School Choice Enhancements: COMPLETED 06/2017- Voting completed prior to October 2015 - Furniture/renovation for the media center; installation completed 06/2017.

SMART Facilities Update By Project



Primary Renovation

Phase: **95% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2015	Q4 2015	Q3 2016	Q2 2018	Q3 2018	Q4 2019 / Q1 2020
New Planned	Q4 2015	Q4 2015	Q3 2016	Q4 2019	Q2 2020	Q3 2021 / Q3 2021
Actual/Forecast	10/29/2015	12/8/2015	9/23/2016	Q4 2020		

SCOPE:	BUDGET:
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$2,710,000
Fire Sprinklers	\$1,482,000
IAQ Repairs - HVAC	\$4,642,000
Media Center improvements	\$88,000

FLAG: S - Project Delayed

COMMENTS:
 Reason: Delays have occurred during the design phase. The design firm has not submitted design documents per the professional service agreement. A redesign of the roofing system was needed prior to permit review. Design is nearing completion of the revision. Remedy: The owner will be enforcing terms of the contract for delays.

Media Center Improvements

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	N/A	N/A	N/A	N/A / N/A
Actual/Forecast	N/A	N/A	N/A	N/A	N/A	N/A / 11/1/2016

SCOPE:	BUDGET:
Media Center improvements - Carpet and Paint	\$30,000

FLAG:

COMMENTS:

Atlantic Technical College & Technical High School

SMART Facilities Update by Project Cont.

School Choice Enhancements*

Phase: **100%** Complete

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2016	N/A	Q2 2017
Actual	01/2016	N/A	06/2017

SCOPE:

School Choice Enhancement

BUDGET:

\$100,000

FLAG:

COMMENTS:

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Coconut Creek Elementary School

500 NW 45 AVENUE, COCONUT CREEK 33066

Location Num	1421
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$5,503,761
Total Facilities Budget	\$5,144,761

***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.


- All dates are based on calendar year. SMART funded projects are included. Only
- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: Complete

Primary Renovation: Complete.

School Choice Enhancements: COMPLETED 02/2019 - Voting completed 2/19/16 - 38 TVs delivered 12/2017; installed 02/2018. Additional TV delivered 02/2018. Playground installation completed 04/2018. TV delivered 08/2018; installed 11/2018. Outdoor benches delivered 09/2018. Table on order 02/2019.

SMART Facilities Update By Project



Primary Renovation

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2015	Q4 2015	Q3 2016	Q1 2017	Q3 2017	Q3 2018
New Planned	Q4 2015	Q4 2015	Q3 2016	Q1 2017	Q3 2017	Q1 2019
Actual/Forecast	10/29/2015	12/8/2015	8/25/2016	5/4/2017	2/26/2018	2/28/2020

SCOPE:	BUDGET:
Additional Funding - Board Approved 12/19/17 (JJ-14)	\$517,143
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,055,000
Fire Alarm	\$294,000
Fire Sprinklers	\$699,000
Media Center improvements	\$274,000
Replace existing unit ventilators (appr. 43 CRs) with new unit ventilators.	\$2,205,618

FLAG:

COMMENTS:



Coconut Creek High School

1400 NW 44 AVENUE, COCONUT CREEK 33066

Location Num	1681
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$5,985,907
Total Facilities Budget	\$4,523,000


***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.
 - All dates are based on calendar year. SMART funded projects are included. Only
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in the permitting process. Building Department is currently reviewing the second submission.

School Choice Enhancements: COMPLETED 03/2020 - Voting authorized 2/9/2018. Voting completed 3/2/2018. Projectors delivered 05/2018. Auditorium Sound System, Cafeteria Tables delivered and installed 08/2018. Laptops carts and (30) laptops delivered 09/2018. Projector screen delivered 03/2019. Additional Cafeteria Tables on order. Auditorium Projector delivered 06/2019. (4) additional cafeteria tables delivered 8/2019. (1) Laptop 100E ordered with the remaining funds.

SMART Facilities Update By Project



Primary Renovation

Phase: **96% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2016	Q2 2016	Q3 2016	Q4 2017	Q2 2018	Q2 2019
New Planned	Q1 2016	Q2 2016	Q3 2016	Q4 2019	Q2 2020	Q3 2021
Actual/Forecast	2/10/2016	4/19/2016	9/23/2016	Q4 2020		

SCOPE:	BUDGET:
Auditorium Accessibility	\$250,000
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$686,000
Fire Alarm	\$1,174,000
HVAC Improvements	\$814,000
Media Center improvements	\$600,000
Safety / Security Upgrade	\$53,000
STEM Lab improvements	\$725,000

FLAG: S - Project Delayed

COMMENTS:

Reason: Delays have occurred during the design phase. The design firm has not met the deadlines of the design deliverables. Remedy: The owner will be enforcing terms of the contract for delays.



Dave Thomas Education Center - West

4690 COCONUT CREEK PARKWAY, COCONUT CREEK 33066


Location Num	2031
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$212,000
Total Facilities Budget	\$100,000

***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.
 - All dates are based on calendar year. SMART funded projects are included. Only
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".


PRIMARY PROJECTS CURRENT STATUS: N/A

School Choice Enhancements: COMPLETED 12/2017 - Voting completed 10/11/16. Reconstructing of Room 202 is completed. Technology items and outdoor furniture delivered and installed 02/2017. Recordex delivered 03/2017. Wall wraps delivered 12/2017.

SMART Facilities Update By Project



School Choice Enhancements*

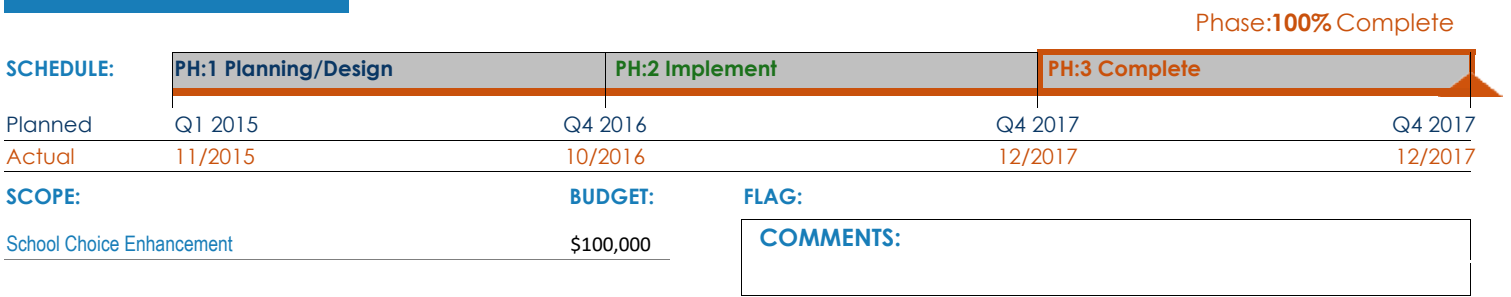

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Lyons Creek Middle School

4333 SOL PRESS BOULEVARD, COCONUT CREEK 33073

Location Num	3101
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$3,767,502
Total Facilities Budget	\$3,149,000


***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.
 - All dates are based on calendar year. SMART funded projects are included. Only
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: Design Scope Validation is in progress.

School Choice Enhancements: Principal's letter initiated 11/30/2018 for Year 5 group. Kick-off meeting held 01/11/2018. Ballot developed and waiting for SAC's approval on 2/19/2019. Voting authorized 2/20/2019. Voting completed 3/11/2019. Digital marquee on order. School name on building installed 5/2019. Aiphone for the Single Point of Entry installation completed 03/2020. Marquee is in design.

SMART Facilities Update By Project



Primary Renovation

Phase: **18% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2018	Q3 2018	Q1 2019	Q4 2019	Q2 2020	Q4 2020
New Planned	Q2 2018	Q3 2018	Q2 2019	Q4 2020	Q3 2021	Q3 2022
Actual/Forecast	9/28/2017	6/27/2018	6/24/2020	Q3 2021		

SCOPE:	BUDGET:
Art Room Renovation and Equipment	\$85,000
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,251,000
Conversion of Existing Space to Music and/or Art Lab(s)	\$928,000
HVAC Improvements	\$264,000
Music Room Renovation	\$521,000

FLAG: S - Delay Possible

COMMENTS:
 Reason: Delays occurred due to additional review of the delivery method and Board approval to perform the project using CMAR services. Remedy: Authorization to Proceed has been executed and the design has begun.

Lyons Creek Middle School

SMART Facilities Update by Project Cont.

School Choice Enhancements*

 Phase: **40% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q4 2018	Q1 2019	TBD
Actual	11/2018	03/2019	TBD

SCOPE:	BUDGET:	FLAG:
School Choice Enhancement	\$100,000	COMMENTS: Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Monarch High School

5050 WILES ROAD, COCONUT CREEK 33073

Location Num	3541
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$3,994,000
Total Facilities Budget	\$2,780,000

***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.


- All dates are based on calendar year. SMART funded projects are included. Only
- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: Design Scope Validation is in progress.

School Choice Enhancements: COMPLETED 09/2020 - Ballot received 12/3/2019. Ballot in compliance with District guidelines; voting authorized. Voting completed 1/28/2020. Embroidery Machine delivered 04/2020. (300) folding tables, (3) table trolley carts, (300) folding chairs and (4) chair carts delivered 03/2020. (8) Picnic Tables delivered 05/2020. (5) Computer carts, (145) Student Laptops delivered 06/2020. Aiphone for the Single Point of Entry completed 09/2020. (2) Golf Carts on order.

SMART Facilities Update By Project



Primary Renovation

Phase: **30% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2018	Q3 2018	Q1 2019	Q4 2019	Q2 2020	Q4 2020
New Planned	Q2 2018	Q3 2018	Q2 2019	Q4 2020	Q3 2021	Q4 2022
Actual/Forecast	9/28/2017	6/27/2018	6/18/2020	Q2 2021		

SCOPE: Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.) HVAC Improvements	BUDGET: \$1,799,000 \$425,000	FLAG: S - Delay Possible COMMENTS: Reason: Delays occurred due to additional review of the delivery method and Board approval to perform the project using CMAR services. Remedy: Authorization to Proceed has been executed and the design has begun.
--	--	--

Weight Room

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q4 2017	Q4 2017	Q4 2017	Q2 2018	Q2 2018	Q3 2018
Actual/Forecast	12/29/2017	1/5/2018	2/5/2018	4/17/2018	4/25/2018	8/3/2018

SCOPE: Weight Room Renovation	BUDGET: \$121,000	FLAG: COMMENTS:
---	-----------------------------	----------------------------------

Monarch High School

SMART Facilities Update by Project Cont.

Track

 Phase: **100%** Complete

SCHEDULE:
 (Calendar Year)

Planned	Q3 2017	Q3 2017	Q3 2017	Q4 2017	Q4 2017	Q1 2018	Q1 2018
Actual/Forecast	8/25/2017	9/1/2017	9/2/2017	10/17/2017	10/25/2017	3/14/2018	3/21/2018

SCOPE:

Track Resurfacing

BUDGET:

\$335,000

FLAG:
COMMENTS:

School Choice Enhancements*

 Phase: **98%** Complete

SCHEDULE:

Planned	PH:1 Planning/Design		PH:2 Implement		PH:3 Complete	
Actual	Q4 2018	Q1 2020	Q3 2020	Q3 2020	Q3 2020	Q3 2020
	11/2018	01/2020	09/2020			09/2020

SCOPE:

School Choice Enhancement

BUDGET:

\$100,000

FLAG:
COMMENTS:

All items approved by voting process have been delivered and installed. School is determining how to spend the remaining funding from the contingency portion of the SCEP funding.

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Tradewinds Elementary School

5400 JOHNSON ROAD, COCONUT CREEK 33073

Location Num	3481
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$4,417,900
Total Facilities Budget	\$3,943,900

***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.


- All dates are based on calendar year. SMART funded projects are included. Only
- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Notice to Proceed execution is pending final signatures.

School Choice Enhancements: Voting authorized 5/20/2019. Voting completed 6/5/2019. FMWO issued to fund an Aiphone at the Single Point of Entry and a Strike at the secondary door on 08/2019. Hardware scope completed 03/2020; Electrical scope pending installation. Playground Upgrades / Rubber Surfacing on order.

SMART Facilities Update By Project



Primary Renovation

Phase: **95% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2018	Q2 2018	Q4 2018	Q3 2019	Q2 2020	Q3 2020
New Planned	Q1 2018	Q2 2018	Q4 2018	Q1 2020	Q2 2020	Q2 2021
Actual/Forecast	11/13/2017	12/19/2017	8/20/2018	1/22/2020	Q4 2020	

SCOPE:	BUDGET:
Additional Funding - Board Approved 7/21/20 (JJ-4)	\$2,132,900
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,205,000
Conversion of Existing Space to Music and/or Art Lab(s)	\$169,000
HVAC Improvements	\$194,000
Music Room Renovation	\$136,000
PE/Athletic Improvements	\$7,000

FLAG: SB - Project Delayed

COMMENTS:

Funding Year 1 thru 3 projects are to take priority for advertisement of bid. The project is funded under Year 4 and will be advertised after the funding Year 1 thru 3 projects that are prepared for advertisement. Budget: Additional funding of \$2,132,900 was approved by the Board on 7/21/2020 in conjunction with the approval to award the construction agreement for the project.

Tradewinds Elementary School

SMART Facilities Update by Project Cont.

School Choice Enhancements*

 Phase: **10%** Complete

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q4 2018	Q2 2019	TBD
Actual	11/2018	06/2019	TBD

SCOPE:	BUDGET:	FLAG:
School Choice Enhancement	\$100,000	COMMENTS: Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Winston Park Elementary School

4000 WINSTON PARK BOULEVARD, COCONUT CREEK 33073

Location Num	3091
Board District	7
Board Member	Nora Rupert
ADEFP Budget*	\$3,051,600
Total Facilities Budget	\$2,444,600

***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.


- All dates are based on calendar year. SMART funded projects are included. Only
- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction in progress. Submittals are being prepare.

School Choice Enhancements: COMPLETED 10/2018 - Voting completed 3/21/18 - Art Tables delivered 06/2018. Recordex, (10) Televisions, and Bulletin Boards delivered 07/2018. (151) Cart wiring delivered 10/2018.

SMART Facilities Update By Project



Primary Renovation

Phase: **1% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q3 2017	Q4 2017	Q3 2018	Q1 2019	Q3 2019	Q2 2020
New Planned	Q3 2017	Q4 2017	Q3 2018	Q4 2019	Q2 2020	Q2 2021
Actual/Forecast	6/1/2017	8/30/2017	3/14/2018	7/12/2019	8/31/2020	9/29/2021

SCOPE:	BUDGET:
Art Room Renovation and Equipment	\$65,000
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$289,000
Conversion of Existing Space to Music and/or Art Lab(s)	\$339,000
Deduction of Funding - Board Approved 5/19/20 (JJ-19)	(\$336,400)
Fire Sprinklers	\$819,000
HVAC Improvements	\$736,000
Music Room Renovation	\$136,000

FLAG: S - Project Delayed

COMMENTS:

Original contractual date of substantial completion is 9/29/2021. Contractor is currently on pace. Previous delays during the bid and award phase will not be recovered.

Winston Park Elementary School

SMART Facilities Update by Project Cont.

Chiller Replacement

 Phase: **95%** Complete

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	N/A	N/A

SCOPE: HVAC Improvements - Chiller Replacement	BUDGET: \$297,000	FLAG: COMMENTS:
--	-----------------------------	----------------------------------

School Choice Enhancements*

 Phase: **100%** Complete

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q4 2017	Q1 2018	Q4 2018
Actual	11/2017	03/2018	10/2018

SCOPE: School Choice Enhancement	BUDGET: \$100,000	FLAG: COMMENTS:
--	-----------------------------	----------------------------------

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.
