



 **SMART INVESTMENTS
LEAD TO SMART STUDENTS.**



MUNICIPAL REPORT

For The Quarter Ending
September 30, 2020 | FY21-Q1



PREFACE

We are pleased to present the updated Broward County Public Schools (BCPS) **School Spotlight** editions specifically designed for city administrators, city commissioners, council-representatives and Broward County School Board Members.

The School Spotlight is a quarterly report that details the progress of facilities projects at each of the 232 schools participating in the SMART Bond Program. This “City Edition” of The School Spotlight provides a municipal breakdown of all approved renovation projects, projected costs, School Choice Enhancement Program initiatives and other ongoing or scheduled SMART Program projects.

These easy-to-read School Spotlights allow board members and city officials to better follow the progress of the facilities improvements within specific municipalities. The Spotlights will be updated every quarter to help city officials and school board members share timely information with business groups, community organizations, homeowners’ associations and other key constituents as ongoing SMART Program projects continue to progress.

SMART (**S**afety, **M**usic & **A**rt, **A**thletics, **R**enovation and **T**echnology) is the **\$800 million capital improvement** program to upgrade existing school facilities and to purchase new computer technology, athletic equipment and musical instruments to enhance the learning experience of Broward County students.



Annabel C. Perry Pre K - 8 (f.k.a. Annabel C. Perry Elementary)

6850 SW 34 STREET, MIRAMAR 33023

Location Num	1631
Board District	1
Board Member	Ann Murray
ADEFP Budget*	\$5,478,037
Total Facilities Budget	\$5,115,037

***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.


- All dates are based on calendar year. SMART funded projects are included. Only
- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction in progress. All work is complete with final inspections pending.

School Choice Enhancements: COMPLETED 05/2018 - Voting completed 5/25/2016. Front office renovation completed 8/2016; (45) student laptops and a golf cart delivered 09/2016; Athletics equipment delivered 10/2016. Outdoor furniture delivered 11/2016. Digital marquee installed and operational 11/2017. Floor mats delivered 11/2017. Front door wrap delivered and installed 12/2017. Minifridge and presentation cabinets delivered 03/2018. Chain link fence art work delivered 05/2018.

SMART Facilities Update By Project



Primary Renovation

Phase: **99% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2016	Q2 2016	Q4 2016	Q4 2017	Q1 2018	Q1 2019
New Planned	Q1 2016	Q2 2016	Q4 2016	Q4 2017	Q1 2018	Q3 2019
Actual/Forecast	3/9/2016	5/17/2016	12/14/2016	2/13/2018	10/16/2018	10/11/2020

SCOPE:	BUDGET:
Additional Funding - Board Approved 05/22/18 (JJ-2)	\$1,950,037
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$967,000
Electrical Improvements	\$294,000
Fire Alarm	\$293,000
Fire Sprinklers	\$18,000
HVAC Improvements	\$1,170,000

FLAG: S - Project Delayed

COMMENTS:
 Original contractual date of substantial completion is 9/18/2019. Reason: Delays occurred due to Fire Alarm Specification Changes and Roofing Contractor Issues with permitting. Remedy: All work is complete with final inspections pending.

Annabel C. Perry Pre K - 8 (f.k.a. Annabel C. Perry Elementary)

SMART Facilities Update by Project Cont.

Media Center

 Phase: **100%** Complete

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2017	Q2 2017	Q1 2018	Q2 2018	Q1 2019	Q4 2019 Q4 2019
New Planned	Q1 2017	Q2 2017	Q1 2018	Q2 2019	Q4 2019	Q2 2021 Q2 2021
Actual/Forecast	3/7/2017	5/11/2017	8/9/2017	1/2/2019	6/6/2019	8/15/2019 11/20/2019
SCOPE:	BUDGET:		FLAG:			
Media Center improvements	\$323,000		<div style="border: 1px solid black; padding: 5px;"> COMMENTS: </div>			

School Choice Enhancements*

 Phase: **100%** Complete

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	Q2 2016	Q1 2018 Q1 2018
Actual	11/2015	05/2016	05/2018 05/2018
SCOPE:	BUDGET:		FLAG:
School Choice Enhancement	\$100,000		<div style="border: 1px solid black; padding: 5px;"> COMMENTS: </div>

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Coconut Palm Elementary School

13601 MONARCH LAKES BOULEVARD, MIRAMAR 33027

Location Num	3741
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$1,599,000
Total Facilities Budget	\$1,156,000

***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.

- All dates are based on calendar year. SMART funded projects are included. Only


- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Pending roof reality check prior to advertisement for bids.

School Choice Enhancements: Voting completed 9/20/16. PIP rubber surfacing completed 02/2017. Basketball shade structure permitted 07/2018; installed 01/2019. Aiphone submaster station installed 04/2019. (1) Recordex and (2) AC adapters delivered 04/2019. Laptops delivered 06/2019. (9) 300e Laptops delivered 09/2020.

SMART Facilities Update By Project



Primary Renovation

 Phase: **5% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2018	Q2 2018	Q1 2019	Q2 2019	Q1 2020	Q2 2020
New Planned	Q1 2018	Q2 2018	Q1 2019	Q1 2020	Q2 2020	Q2 2021
Actual/Forecast	8/1/2017	10/6/2017	3/22/2018	6/4/2020	Q3 2021	

SCOPE:	BUDGET:
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$746,000
Fire Alarm	\$42,000
HVAC Improvements	\$268,000

FLAG: S - Project Delayed
COMMENTS:

Reason: Delays occurred during the design phase related to permitting. Additional testing on the roofing system was required in order to submit for a sixth review to the Building Department. Remedy: Letter of Recommendation to Permit has been received. Pending roof reality check prior to advertisement for bids.

Coconut Palm Elementary School

SMART Facilities Update by Project Cont.

School Choice Enhancements*

 Phase: **100%** Complete

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	Q3 2016	Q2 2018
Actual	11/2015	09/2016	07/2019

SCOPE:

School Choice Enhancement

BUDGET:

\$100,000

FLAG:
COMMENTS:

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Coral Cove Elementary School

5100 SW 148 AVENUE, MIRAMAR 33027

Location Num	2011
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$698,000
Total Facilities Budget	\$248,000


***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.
 - All dates are based on calendar year. SMART funded projects are included. Only
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS:

Primary Renovation: Test and Balance services is completed by a licensed contractor without standard design services. Test and Balance report submitted. Final repairs are pending prior to completion of the project.

School Choice Enhancements: COMPLETED 01/2017. Voting completed 10/12/16. (46) LCD projectors delivered and ceiling mounted. Projects complete 1/25/17.

SMART Facilities Update By Project



Primary Renovation

Phase: **10% Complete**

SCHEDULE: (Calendar Year)	Closeout						
Planned	Q4 2017	N/A	N/A	Q2 2019	Q4 2019	Q1 2020	Q1 2020
New Planned	Q4 2017	N/A	N/A	Q2 2019	Q4 2019	Q1 2020	Q1 2020
Actual/Forecast	5/1/2017	N/A	N/A	1/10/2018	4/27/2018	7/1/2019	10/15/2020

SCOPE: HVAC Improvements **BUDGET:** \$148,000 **FLAG:**

COMMENTS:
 Substantial completion percentage was reduced to 10% from 90%. Additional repairs are required that will delay the completion of the project.

School Choice Enhancements*

Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	Q4 2016	Q1 2017
Actual	11/2015	10/2016	01/2017

SCOPE: School Choice Enhancement **BUDGET:** \$100,000 **FLAG:**

COMMENTS:

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Dolphin Bay Elementary School

16450 MIRAMAR PARKWAY, MIRAMAR 33027

Location Num	3751
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$307,000
Total Facilities Budget	\$100,000

***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.
 - All dates are based on calendar year. SMART funded projects are included. Only
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".


PRIMARY PROJECTS CURRENT STATUS: N/A

School Choice Enhancements: COMPLETED 04/2019 - Voting completed 3/24/17. Projectors delivered 05/2017. Morning Announcement Studio Equipment, Recordex, Laptops delivered 8/2017. Playground upgrades, new play equipment Pre-K installed 12/2018. (1) Laptop, (8) Projectors and (1) ThinkPad delivered 04/2019.

SMART Facilities Update By Project



School Choice Enhancements*

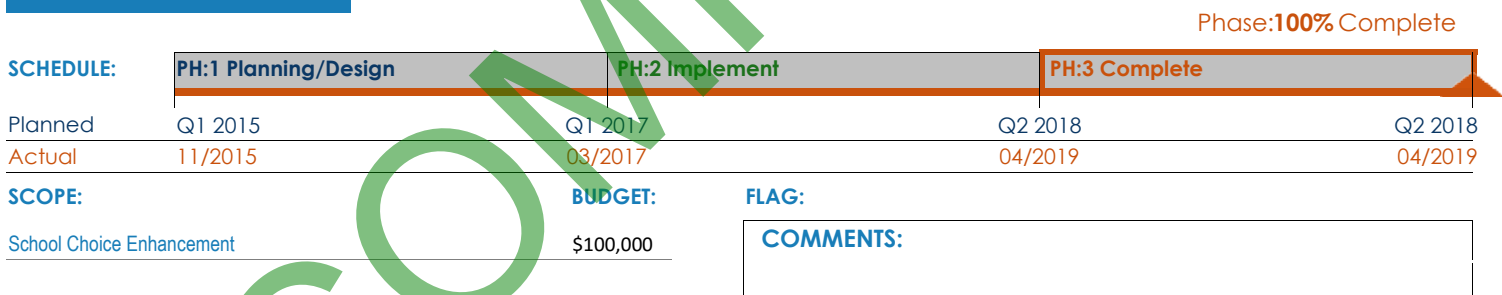

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Everglades High School

17100 SW 48 COURT, MIRAMAR 33027

Location Num	3731
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$8,040,254
Total Facilities Budget	\$6,597,254


***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.
 - All dates are based on calendar year. SMART funded projects are included. Only
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction in progress. Test and Balance is in progress. Roofing and HVAC upgrades are complete. Leak detection system has been installed.

School Choice Enhancements: COMPLETED 03/2018 - Voting authorized 11/28/17 - Voting completed 12/19/17 - (330) laptops delivered 03/2018. (6) Printers delivered 02/2018.

SMART Facilities Update By Project



Primary Renovation

Phase: **98% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2017	Q2 2017	Q1 2018	Q3 2018	Q1 2019	Q1 2020
New Planned	Q2 2017	Q2 2017	Q1 2018	Q2 2019	Q3 2019	Q3 2021
Actual/Forecast	4/14/2017	5/19/2017	12/4/2017	4/3/2019	8/30/2019	11/30/2020

SCOPE:

Additional Funding - Board Approved 08/06/19 (JJ-3)
 Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)
 HVAC Improvements

BUDGET:

\$2,707,254
 \$2,794,000
 \$875,000

FLAG:

COMMENTS:

Original contractual date of substantial completion is 1/2/2021. Project is currently on pace.

Weight Room

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2017	Q2 2017	Q3 2017	Q3 2017	Q3 2017	Q4 2017
Actual/Forecast	5/5/2017	5/12/2017	7/13/2017	8/2/2017	11/12/2017	1/10/2018

SCOPE:

Weight Room Renovation

BUDGET:

\$121,000

FLAG:

COMMENTS:

Everglades High School

SMART Facilities Update by Project Cont.

School Choice Enhancements*

 Phase: **100%** Complete

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	Q4 2017	Q1 2018
Actual	11/2015	12/2017	03/2018

SCOPE:

School Choice Enhancement

BUDGET:

\$100,000

FLAG:
COMMENTS:

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Fairway Elementary School

7850 FAIRWAY BOULEVARD, MIRAMAR 33023

Location Num	1641
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$7,891,900
Total Facilities Budget	\$7,610,900

***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.


- All dates are based on calendar year. SMART funded projects are included. Only
- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction in progress. Site lighting and courtyard area sitework is complete. Stucco work for Building 75 is complete. HVAC renovations in cafeteria is nearing completion. Roofing work is in progress.

School Choice Enhancements: COMPLETED 03/2020 - Voting completed 9/2/16. Color poster maker delivered 10/2016. Two-way radios, projectors and document cameras delivered 12/2016. Morning show equipment delivered 01/2017. Sound Stage Projector delivered 11/2017. Cafeteria Sound system delivered 01/2018. Microphones for the sound system installed 02/2018. (30) laptops delivered 04/2018. Marquee completed 08/2018. (3) ThinkPads delivered 12/2018. One laptop and adaptors delivered 08/2019. TV installation completed 05/2019. (1) Desktop M820z delivered 02/2020.

SMART Facilities Update By Project



Primary Renovation

Phase: **73% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2016	Q2 2016	Q1 2017	Q4 2017	Q1 2018	Q1 2019
New Planned	Q2 2016	Q2 2016	Q1 2017	Q1 2019	Q2 2019	Q4 2020
Actual/Forecast	4/18/2016	6/15/2016	2/6/2017	1/18/2019	6/25/2019	12/19/2020

SCOPE:	BUDGET:
Additional Funding - Board Approved 05/07/19 (JJ-2)	\$3,507,900
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$1,408,000
Electrical Improvements	\$366,000
Fire Alarm	\$294,000
HVAC Improvements	\$1,570,000
Media Center improvements	\$172,000
Safety / Security Upgrade	\$193,000

FLAG: S - Delay Possible

COMMENTS:
 Original contractual date of substantial completion is 8/14/2020. Project is currently delayed by 4 months due to the pace of work during the health crisis.

Fairway Elementary School

SMART Facilities Update by Project Cont.

School Choice Enhancements*

Phase: **100%** Complete

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2016	Q4 2016	Q1 2020
Actual	01/2016	09/2016	02/2020

SCOPE:

School Choice Enhancement

BUDGET:

\$100,000

FLAG:

COMMENTS:

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Glades Middle School

16700 SW 48 COURT, MIRAMAR 33027

Location Num	2021
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$892,000
Total Facilities Budget	\$486,000


***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.
 - All dates are based on calendar year. SMART funded projects are included. Only
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Pending scope decisions by the District prior to continuing with the contractor procurement.

School Choice Enhancements: COMPLETED 05/2018 - Voting completed 1/23/17. Apple iPads, books delivered 08/2017. Tablets delivered 09/2017. Recordex, Laptops and P.E. Equipment delivered 10/2017. Camera for TV Production system delivered 11/2017. Technology supplies delivered 03/2018. HDMI cables delivered 05/2018.

SMART Facilities Update By Project



Primary Renovation

Phase: **50% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2017	Q2 2017	Q1 2018	Q3 2018	Q1 2019	Q4 2019
New Planned	Q2 2017	Q2 2017	Q1 2018	Q1 2019	Q3 2019	Q3 2020
Actual/Forecast	4/6/2017	4/19/2017	11/17/2017	1/25/2019	Q2 2021	

SCOPE:	BUDGET:
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$78,000
HVAC Improvements	\$308,000

FLAG: S - Project Delayed

COMMENTS:

Reason: Delays have occurred during the Bid and Award phase due to difficulties in receiving correct quotes from multiple contractors. Remedy: Decisions will be required by the District related to the scope of the project. There is a potential cost savings thru value engineering of the design.

Glades Middle School

SMART Facilities Update by Project Cont.

School Choice Enhancements*

 Phase: **100%** Complete

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete	
Planned	Q1 2015	Q1 2017	Q4 2017	Q4 2017
Actual	11/2015	01/2017	05/2018	05/2018

SCOPE:


School Choice Enhancement

BUDGET:

\$100,000

FLAG:
COMMENTS:

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.

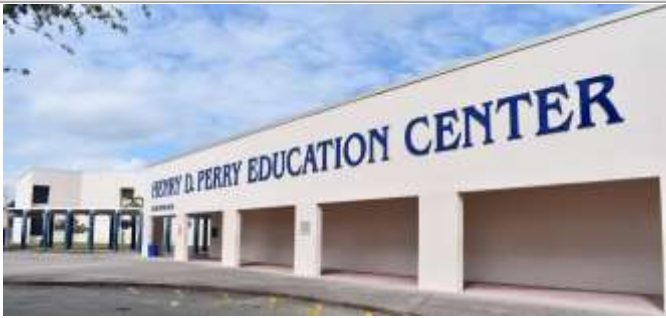

Henry D. Perry Education Center

3400 WILDCAT WAY, MIRAMAR 33023

Location Num	1011
Board District	1
Board Member	Ann Murray
ADEFP Budget*	\$9,720,580
Total Facilities Budget	\$9,408,580


***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.
 - All dates are based on calendar year. SMART funded projects are included. Only
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Pending final signatures for the Notice to Proceed with Construction.

School Choice Enhancements: Voting completed 2/15/2019 - Indoor furniture, cafeteria tables delivered 08/2019. Students chairs and desks delivered 08/2019. Laptop carts delivered 10/2019.

SMART Facilities Update By Project



Primary Renovation

Phase: **95% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2017	Q2 2017	Q1 2018	Q3 2018	Q1 2019	Q2 2020
New Planned	Q2 2017	Q2 2017	Q1 2018	Q3 2019	Q1 2020	Q2 2021
Actual/Forecast	4/14/2017	5/19/2017	12/7/2017	5/20/2019	Q4 2020	

SCOPE:	BUDGET:
Additional Funding - Board Approved 8/19/20 (JJ-6)	\$3,501,580
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$2,145,000
Fire Alarm	\$461,000
Fire Sprinklers	\$15,000
HVAC Improvements	\$3,186,000

FLAG: SB - Project Delayed

COMMENTS:

Funding Year 1 thru 3 projects are to take priority for advertisement of bid. The project is funded under Year 4. Advertisement for bids took place with all available Year 1 thru 3 projects already advertised. Pending final signatures for the Notice to Proceed with Construction. Budget: Additional funding of \$3,501,580 was approved by the Board on 8/19/2020 in conjunction with the approval to award the construction agreement for the project.

Henry D. Perry Education Center

SMART Facilities Update by Project Cont.

School Choice Enhancements*

 Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q4 2017	Q1 2019	Q3 2020
Actual	11/2017	02/2019	10/2019

SCOPE:

School Choice Enhancement

BUDGET:

\$100,000

FLAG:
COMMENTS:

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Miramar Elementary School

6831 SW 26 STREET, MIRAMAR 33023

Location Num	0531
Board District	1
Board Member	Ann Murray
ADEFP Budget*	\$6,557,935
Total Facilities Budget	\$6,184,935


***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.
 - All dates are based on calendar year. SMART funded projects are included. Only
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: Complete

Primary Renovation: Substantial Completion has been reached. Project closeout is in progress with minor HVAC improvements needed to closeout the project. Final installation has taken place with system testing in progress.

School Choice Enhancements: COMPLETED 08/2018 - Voting completed 5/5/17: (75) student laptops and safety cones delivered 07/2017. (13) document cameras, stage curtains delivered 08/2017. Cafeteria sound system delivered and installed 12/2017. Picnic tables and cafeteria blinds delivered and installed 01/2018. Office furniture delivered 07/2018. Permit for the marquee issued 2/2/2018; Marquee installed 07/2018 and electrical tie-in completed 08/2018.

SMART Facilities Update By Project



Primary Renovation

Phase: **80% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2016	Q2 2016	Q4 2016	Q3 2017	Q1 2018	Q1 2019
New Planned	Q1 2016	Q2 2016	Q4 2016	Q3 2017	Q4 2018	Q1 2020
Actual/Forecast	3/9/2016	5/17/2016	12/13/2016	6/15/2018	11/30/2018	11/20/2019

SCOPE:	BUDGET:
Additional Funding - Board Approved 11/07/18 (JJ-1)	\$2,286,935
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$855,000
HVAC Improvements	\$2,943,000

FLAG:	COMMENTS:

School Choice Enhancements*

Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	Q2 2017	Q2 2018
Actual	11/2015	05/2017	08/2018

SCOPE:	BUDGET:
School Choice Enhancement	\$100,000

FLAG:	COMMENTS:

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Miramar High School

3601 SW 89 AVENUE, MIRAMAR 33025

Location Num	1751
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$12,674,000
Total Facilities Budget	\$11,528,000


***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.
 - All dates are based on calendar year. SMART funded projects are included. Only
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: Hire Contractor

Primary Renovation: Contractor procurement in progress. Pending advertisement for bid.

School Choice Enhancements: COMPLETED 01/2020 - Voting completed 12/7/18 - Additional parking spaces on order. Golf Cart delivered 03/2019. Additional security cameras, Scrubber Machine and protective mats for gym floor delivered 04/2019. Canopy fabric installed 05/2019. Auditorium painting and signage for the gym and stadium completed 7/2019. Additional parking spaces project was permitted 08/2019; construction began 11/2019; project completed 1/2020.

SMART Facilities Update By Project



Primary Renovation

Phase: **5% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2017	Q2 2017	Q1 2018	Q4 2018	Q3 2019	Q4 2020
New Planned	Q2 2017	Q2 2017	Q1 2018	Q4 2019	Q1 2020	Q4 2021
Actual/Forecast	4/1/2017	6/22/2017	1/8/2018	8/19/2020	Q1 2021	

SCOPE:	BUDGET:
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$966,000
Conversion of Existing Space to Music and/or Art Lab(s)	\$302,000
Electrical Improvements	\$792,000
Fire Alarm	\$1,174,000
Fire Sprinklers	\$45,000
HVAC Improvements	\$5,301,000
Media Center improvements	\$870,000
Music Room Renovation	\$713,000
STEM Lab improvements	\$844,000

FLAG: S - Project Delayed

COMMENTS:

Reason: Delays have occurred in the design phase due to an above average amount of submissions for permit review. Remedy: The owner will be enforcing terms of the contract for delays and multiple resubmissions.



New Renaissance Middle School

10701 MIRAMAR BOULEVARD, MIRAMAR 33027

Location Num	3911
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$4,046,000
Total Facilities Budget	\$3,654,000

***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.


- All dates are based on calendar year. SMART funded projects are included. Only
- Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: Schematic Design Documents are in review.

School Choice Enhancements: Voting authorized 3/14/2019. Voting results received on 4/29/2019. Aiphone at the main entrance and strike at the secondary door on order, replacing locks in certain areas completed 10/2019. Wall wraps delivered 12/2019.

SMART Facilities Update By Project



Primary Renovation

Phase: **25% Complete**

SCHEDULE: (Calendar Year)	1: Planning		2: Hire Design Team		3: Design		4: Hire Contractor		5: Construction		6: Closeout	
Planned	Q2 2018	Q3 2018	Q1 2019	Q4 2019	Q2 2020	Q4 2020	Q4 2020	Q2 2021	Q3 2021	Q1 2023	Q4 2020	Q4 2020
New Planned	Q2 2018	Q3 2018	Q2 2019	Q4 2020	Q3 2021	Q1 2023	Q1 2023	Q1 2023	Q1 2023	Q1 2023	Q1 2023	Q1 2023
Actual/Forecast	9/28/2017	6/27/2018	6/7/2020	Q2 2021								

SCOPE:	BUDGET:	FLAG: S - Delay Possible
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$3,276,000	COMMENTS: Reason: Delays occurred due to additional review of the delivery method and Board approval to perform the project using CMAR services. Remedy: Authorization to Proceed has been executed and the design has begun.
HVAC Improvements	\$278,000	

School Choice Enhancements*

Phase: **20% Complete**

SCHEDULE:	PH:1 Planning/Design		PH:2 Implement		PH:3 Complete	
Planned	Q4 2018	Q2 2019	TBD	TBD	TBD	TBD
Actual	11/2018	05/2019				

SCOPE:	BUDGET:	FLAG:
School Choice Enhancement	\$100,000	COMMENTS: Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Sea Castle Elementary School

9600 MIRAMAR BOULEVARD, MIRAMAR 33025

Location Num	2871
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$4,768,154
Total Facilities Budget	\$4,419,154


***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.
 - All dates are based on calendar year. SMART funded projects are included. Only
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction in progress. Roofing of Building 80 is complete. ADA chairlift installation in progress. Underground trenching for fire alarm installation is complete. Fire Alarm installation is pending additional shop drawing approval. HVAC work is nearing completion in Building 6. Building 5 HVAC is in progress.

School Choice Enhancements: COMPLETED 09/2018 - Voting completed in 2015 without OFC's approval. Furniture delivered 4/2017. Office furniture renovation completed 02/2017. Marquee installed 10/2017, and electrical tie-in completed 11/2017. Shade structure completed 11/2017. Science tables, Projector delivered 02/2018. Cafeteria sound system delivered 03/2018. (7) Laptops chargers are delivered 09/2018.

SMART Facilities Update By Project



Primary Renovation

Phase: **50%** Complete

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2016	Q2 2016	Q4 2016	Q3 2017	Q1 2018	Q1 2019
New Planned	Q1 2016	Q2 2016	Q4 2016	Q1 2019	Q2 2019	Q2 2020
Actual/Forecast	3/9/2016	5/17/2016	12/13/2016	4/30/2019	12/13/2019	3/30/2021

SCOPE:	BUDGET:
ADA Stage Lift	\$118,975
Additional Funding - Board Approved 10/15/19 (JJ-2)	\$1,508,179
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$200,000
Fire Alarm	\$252,000
HVAC Improvements	\$1,623,121

FLAG: S - Project Delayed

COMMENTS:
 Original contractual date of substantial completion is 11/12/2020. Project is currently delayed by one month due to additional shop drawing approvals. Delays were experienced during the design phase and the bid and award phase which have not been recovered.

Sea Castle Elementary School

SMART Facilities Update by Project Cont.

Cooling Tower Replacement

 Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	4/26/2017	6/1/2017	8/1/2017

SCOPE: HVAC Improvements - Cooling Tower Replacement	BUDGET: \$233,000	FLAG: COMMENTS:
--	-----------------------------	----------------------------------

Chiller Replacement

 Phase: **100% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	N/A	N/A	N/A	N/A	N/A	N/A
Actual/Forecast	N/A	N/A	N/A	N/A	3/1/2017	7/1/2017

SCOPE: HVAC Improvements - Chiller Replacement	BUDGET: \$383,879	FLAG: COMMENTS:
--	-----------------------------	----------------------------------

School Choice Enhancements*

 Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	Q2 2017	Q1 2018
Actual	11/2015	04/2017	09/2018

SCOPE: School Choice Enhancement	BUDGET: \$100,000	FLAG: COMMENTS:
--	-----------------------------	----------------------------------

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Silver Shores Elementary School

1701 SW 160 AVENUE, MIRAMAR 33027


Location Num	3581
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$2,610,560
Total Facilities Budget	\$2,365,560

***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.
 - All dates are based on calendar year. SMART funded projects are included. Only
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

Primary Renovation: Complete.

School Choice Enhancements: COMPLETED 02/2019 - Revoting completed 05/2016. Student laptops delivered 09/2016. Classroom furniture delivered 07/2017. Additional furniture for computer lab and related arts delivered 11/2017. Additional laptops (15) delivered 05/2018. Electric strike and proximity pad installed 06/2018. Shades installation completed 06/2018. Student furniture for the media center delivered 02/2019.

SMART Facilities Update By Project



Primary Renovation

Phase: **100% Complete**

SCHEDULE: (Calendar Year)	[Timeline bar showing completion from Q1 2019 to Q1 2019]						
Planned	Q4 2016	Q4 2016	Q1 2017	Q3 2017	Q2 2018	Q1 2019	Q1 2019
New Planned	Q4 2016	Q4 2016	Q1 2017	Q3 2017	Q1 2019	Q4 2019	Q1 2020
Actual/Forecast	12/14/2016	12/14/2016	3/6/2017	8/9/2018	1/17/2019	10/18/2019	10/18/2019
SCOPE:	BUDGET:		FLAG:				
Additional Funding - Board Approved 12/04/18 (JJ-2)	\$1,231,560		COMMENTS:				
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$890,000						
HVAC Improvements	\$144,000						

School Choice Enhancements*

Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design		PH:2 Implement		PH:3 Complete	
Planned	Q1 2015	Q2 2016	Q2 2018	Q2 2018	Q2 2018	Q2 2018
Actual	11/2015	05/2016	02/2019	02/2019	02/2019	02/2019
SCOPE:	BUDGET:		FLAG:			
School Choice Enhancement	\$100,000		COMMENTS:			

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Sunset Lakes Elementary School

18400 SW 25 STREET, MIRAMAR 33027

Location Num	3661
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$3,427,500
Total Facilities Budget	\$3,091,500


***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.
 - All dates are based on calendar year. SMART funded projects are included. Only
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction is in progress. HVAC work has been completed. Roofing work is complete. Pending final inspections prior to receiving a Certificate of Occupancy.

School Choice Enhancements: COMPLETED 04/2019 - Voting conducted and completed prior to 10/2015. New PreK-2 playground; shades for 3-5 play area permitted on 1/23/2018; fabrication in progress. Pre-construction meeting held 2/21/2019. Fencing to separate the two play areas installation completed 03/2019. Playground installation started 3/26/2019; construction complete 04/2019.

SMART Facilities Update By Project



Primary Renovation

Phase: **95% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2017	Q2 2017	Q4 2017	Q3 2018	Q1 2019	Q4 2019
New Planned	Q2 2017	Q2 2017	Q4 2017	Q2 2019	Q1 2020	Q1 2021
Actual/Forecast	4/6/2017	4/19/2017	11/20/2017	2/22/2019	10/17/2019	10/8/2020

SCOPE:	BUDGET:
Additional Funding - Board Approved 08/20/19 (JJ-2)	\$1,780,500
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$853,000
HVAC Improvements	\$358,000

FLAG:	COMMENTS:
	Original contractual date of substantial completion is 10/24/2020. Project is currently on pace.

School Choice Enhancements*

Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	N/A	Q2 2018
Actual	11/2015	N/A	04/2019

SCOPE:	BUDGET:
School Choice Enhancement	\$100,000

FLAG:	COMMENTS:

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Sunset Lakes Elementary School

18400 SW 25 STREET, MIRAMAR 33027

Location Num	3661
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$3,427,500
Total Facilities Budget	\$3,091,500


***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.
 - All dates are based on calendar year. SMART funded projects are included. Only
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: **Construction**

Primary Renovation: Construction is in progress. HVAC work has been completed. Roofing work is complete. Pending final inspections prior to receiving a Certificate of Occupancy.

School Choice Enhancements: COMPLETED 04/2019 - Voting conducted and completed prior to 10/2015. New PreK-2 playground; shades for 3-5 play area permitted on 1/23/2018; fabrication in progress. Pre-construction meeting held 2/21/2019. Fencing to separate the two play areas installation completed 03/2019. Playground installation started 3/26/2019; construction complete 04/2019.

SMART Facilities Update By Project



Primary Renovation

Phase: **95% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q2 2017	Q2 2017	Q4 2017	Q3 2018	Q1 2019	Q4 2019
New Planned	Q2 2017	Q2 2017	Q4 2017	Q2 2019	Q1 2020	Q1 2021
Actual/Forecast	4/6/2017	4/19/2017	11/20/2017	2/22/2019	10/17/2019	10/8/2020

SCOPE:	BUDGET:
Additional Funding - Board Approved 08/20/19 (JJ-2)	\$1,780,500
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$853,000
HVAC Improvements	\$358,000

FLAG:	COMMENTS:
	Original contractual date of substantial completion is 10/24/2020. Project is currently on pace.

School Choice Enhancements*

Phase: **100% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q1 2015	N/A	Q2 2018
Actual	11/2015	N/A	04/2019

SCOPE:	BUDGET:
School Choice Enhancement	\$100,000

FLAG:	COMMENTS:

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Sunshine Elementary School

7737 W LASALLE BOULEVARD, MIRAMAR 33023

Location Num	1171
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$1,600,000
Total Facilities Budget	\$1,266,000


***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.
 - All dates are based on calendar year. SMART funded projects are included. Only
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in review. The renovation scope for Building 3 is under review by the District. Decision to be made on demolishing Building 3 or continuing with renovations. Additional meetings with District staff are needed to reach consensus and final direction. Design will be submitted for Permit review without the Building 3 scope of work.

School Choice Enhancements: Voting authorized 4/12/2019. Voting completed 5/1/2019 - Fans, and (4) recordex are on order. Poster maker, (1200) Headphones, Laminator delivered 7/2019. (76) classroom rugs, (4) Portable Blowers delivered 08/2019. (75) Lenovo 100e, (6) Lenovo ThinkPad, (4) Earthwalk Cart, (2) Lenovo Staff Desktop, (2) Lenovo Student Desktop, (26) Student Chairs, (3) Shelving, (35) Bookcase, (35) Pro Pencil Sharpeners, Ellison machine delivered 09/2019. (4) Recordex delivered 10/2019.

SMART Facilities Update By Project



Primary Renovation

Phase: **93% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2018	Q2 2018	Q4 2018	Q2 2019	Q4 2019	Q2 2020
New Planned	Q1 2018	Q2 2018	Q4 2018	Q1 2020	Q2 2020	Q3 2021
Actual/Forecast	8/1/2017	10/6/2017	5/4/2018	Q1 2021		

SCOPE:	BUDGET:
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$211,000
Fire Alarm	\$51,000
Fire Sprinklers	\$532,000
HVAC Improvements	\$372,000

FLAG: S - Project Delayed

COMMENTS:

The project included the demolition or renovation of Building 3. The project is pending the Board decision on demolition or renovation prior to completing the design. District has advised for the project to be submitted for Permit review without the Building 3 scope of work.

Sunshine Elementary School

SMART Facilities Update by Project Cont.

School Choice Enhancements*

Phase: **77% Complete**

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q4 2018	Q2 2019	TBD
Actual	11/2018	05/2019	TBD

SCOPE:	BUDGET:	FLAG:
School Choice Enhancement	\$100,000	COMMENTS: Planned dates shown as TBD will be provided after all items have been ordered and funds allocated.

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.



Whispering Pines Education Center

3609 SW 89TH AVENUE, MIRAMAR 33025


Location Num	1752
Board District	2
Board Member	Patricia Good
ADEFP Budget*	\$2,849,466
Total Facilities Budget	\$2,200,000

***NOTE** This quarter reflects the Adopted District Educational Facilities Plan total budget as approved by SBBC in September 2019. This budget includes Technology improvements and Musical Instruments Replacements which are not included in this section of the report.
 - All dates are based on calendar year. SMART funded projects are included. Only
 - Projects without expenditures to date may not show up in the "Financially Active Project Detail Schedule".

PRIMARY PROJECTS CURRENT STATUS: Design

Primary Renovation: 100% Construction Documents in the permitting process. Building Department is currently reviewing the fourth submissions for permit.
 School Choice Enhancements: Kick-off meeting held 2/19/2019. Ballot Development in progress.

SMART Facilities Update By Project



Primary Renovation

Phase: **98% Complete**

SCHEDULE: (Calendar Year)	1: Planning	2: Hire A/E	3: Design	4: Hire Contractor	5: Construction	6: Closeout
Planned	Q1 2018	Q2 2018	Q1 2019	Q3 2019	Q2 2020	Q3 2020
New Planned	Q1 2018	Q2 2018	Q1 2019	Q4 2019	Q2 2020	Q1 2021
Actual/Forecast	8/1/2017	10/6/2017	3/26/2018	Q4 2020		

SCOPE:	BUDGET:
Bldg Envelope Impr. (Roof, Window, Ext Wall, etc.)	\$837,000
Fire Alarm	\$462,000
Fire Sprinklers	\$11,000
HVAC Improvements	\$790,000

FLAG: S - Project Delayed

COMMENTS:
 Reason: Delays have occurred during the design phase. The design firm has been delayed in meeting the contract schedule. Remedy: The owner will be enforcing terms of the contract for delays.

Whispering Pines Education Center

SMART Facilities Update by Project Cont.

School Choice Enhancements*

Phase: **25%** Complete

SCHEDULE:	PH:1 Planning/Design	PH:2 Implement	PH:3 Complete
Planned	Q4 2018	TBD	TBD
Actual	11/2018		

SCOPE:	BUDGET:	FLAG:
School Choice Enhancement	\$100,000	<p>COMMENTS:</p> <p>Planned date for Implementation phase shown as TBD will be provided after voting process has been completed by the school community.</p>

*SCEP projects follows a three-phase design process that begins with planning/design, followed by implementation and finally completion when all items have been delivered and installed.
