



Established 1915

BROWARD
County Public Schools

**SAFETY
MUSIC & ART
ATHLETICS
RENOVATION
TECHNOLOGY**

District Board Member:

Torey Alston



DISTRICT 2 REPORT

For The Quarter Ending
September 30, 2022 | FY23 Q1

PREFACE

We are pleased to present the Broward County Public Schools (BCPS) **School Spotlights** specifically designed for our School Board Members serving in county-wide school districts.

SMART (**S**afety, **M**usic & **A**rt, **A**thletics, **R**enovation and **T**echnology) is the **\$800 million capital improvement program** to upgrade existing school facilities and to purchase new computer technology, athletic equipment and musical instruments to enhance the learning experience of Broward County students.

The **School Spotlight** is a quarterly report that details the progress of facilities projects at each of the 232 schools participating in the *SMART Bond Program*. This District Board Member edition provides a school-district breakdown of all approved renovation projects, projected costs, School Choice Enhancement Program initiatives and other ongoing or scheduled SMART Program projects.

These easy-to-read School Spotlights allow board members to better follow the progress of the facilities improvements within their specific school districts. The Spotlights will be updated every quarter to help board members share timely information with parents, students, school staff, volunteers, business groups, community organizations and other stakeholders as the projects progress.

Chapel Trail Elementary School



Address: 19595 TAFT STREET, PEMBROKE PINES 33029
 Location Num: 2961
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$5,144,043
 Total Facilities Budget (Sum of Projects): \$4,538,436

PRIMARY RENOVATIONS P.001732 Chapel Trail ES - SMART Program Renovations

CURRENT PHASE

5-Construction

RISK LEVEL



PROJECT UPDATE

110 b in progress, All Scope is completed.


PROJECT SCOPE

Building Envelope Improvements & HVAC Improvements, Walkway replacement

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$328,444	\$304,154	\$24,290
Construction	\$3,168,724	\$3,122,756	\$45,968
Direct Purchase	\$573,157	\$553,885	\$19,272
Construction Mgmt	\$325,713	\$325,713	\$0
Contingency	\$137,518		\$137,518
Consultants	\$4,880		\$4,880
Project Total:	\$4,538,436	\$4,306,508	\$231,928

FLAG: SCHEDULE, Reason:Owner Delays

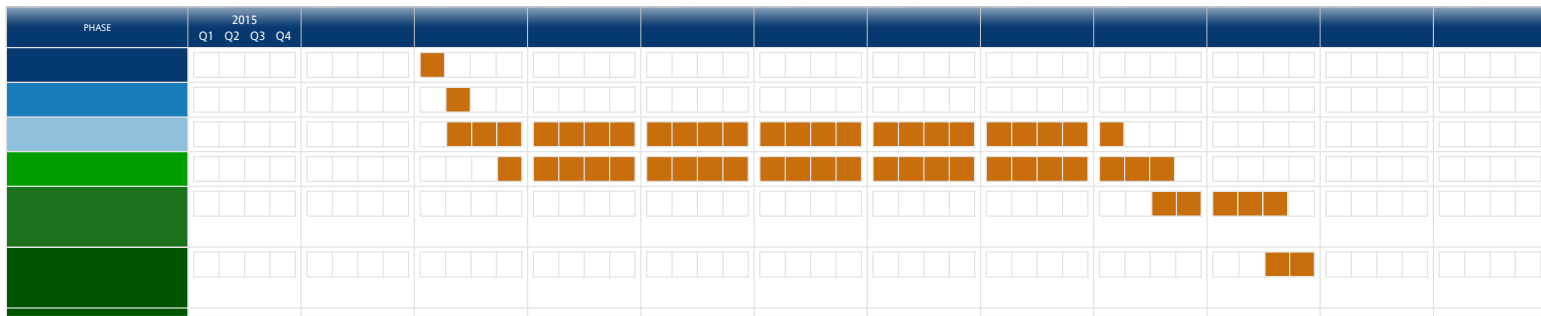

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Student laptops, Stage curtains, Bus loop shade, Shade structure

BUDGET

\$100,000

ATHLETICS

✓ COMPLETE

SCOPE
NULL

MUSIC

✓ COMPLETE

SCOPE
280 Instruments Delivered

TECHNOLOGY

✓ COMPLETE

SCOPE
324 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Charles W. Flanagan High School



Address: 12800 TAFT STREET, PEMBROKE PINES 33028
 Location Num: 3391
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$17,903,461
 Total Facilities Budget (Sum of Projects): \$15,326,362

PRIMARY RENOVATIONS P.001847 Charles W. Flanagan HS - SMART Program Renovations

CURRENT PHASE

6- Substantial Completion/Closeout

RISK LEVEL



PROJECT UPDATE

All change orders are complete. A recently discovered water intrusion problem. The water issue is being evaluated and once the issue has passed the final inspection, the Certificate of Final Inspection will be issued.

PROJECT SCOPE

Aluminum Covered Walkways Replacement: Campus-wide Classroom Addition Aluminum Window Replacement: Buildings 1, 2, 3 & 9 Re-roofing: Buildings 3 (including new decking), 5 (including new decking), 7 & 8 (including new decking) HVAC Improvements: Buildings 1, (Test & Balance), 2 (Exhaust Hoods, Roof Condenser, and Test & Balance), 3 (Circulating Pump, Chiller & Cooling Tower) 4 (Test & Balance), 5 (Test & Balance), 6 (Test & Balance), 8 (Exhaust Fan & Test & Balance), 9 (Test & Balance), & 11 (Controls, Electric Heater, Window AC Unit)

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$590,000	\$570,064	\$19,936
Construction	\$10,307,234	\$9,189,030	\$1,118,204
FF&E and Technology	\$739,335	\$739,192	\$143
Direct Purchase	\$1,722,818	\$1,682,143	\$40,675
Construction Mgmt	\$1,814,895	\$1,783,895	\$31,000
Contingency	\$129,507	\$129,507	\$0
Consultants	\$22,573	\$13,497	\$9,076
Project Total:	\$15,326,362	\$13,977,821	\$1,348,541

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Floor scrubber, Hedger, Trimmer, Blower, Two-way radios, ID machine, Recorderx, Golf carts, Two-way radio batteries, Digital marquee, Office furniture

BUDGET

\$100,000

ATHLETICS

COMPLETE

SCOPE

Track, Weight Room

MUSIC

COMPLETE

SCOPE

210 Instruments Delivered

TECHNOLOGY

COMPLETE

SCOPE

600 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Coconut Palm Elementary School



Address: 13601 MONARCH LAKES BOULEVARD, MIRAMAR 33027
 Location Num: 3741
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$3,243,215
 Total Facilities Budget (Sum of Projects): \$2,700,300

PRIMARY RENOVATIONS P.002088 Coconut Palm ES - SMART Program Renovations

CURRENT PHASE

5-Construction

RISK LEVEL

No Risk

PROJECT UPDATE

Cleanup of interior fireproofing debris, which had been dislodged during demolition phase, has been completed. Obtained permission from Building Department and completed the installation of three scuppers to prevent school entry flooding. Weather antennae relocated and installed. Scupper and metal work is ongoing. Fire Alarm Rough at Media Center is in progress.

PROJECT SCOPE

Electrical Improvements: Building 1 Fascia Repair: Buildings 1, Testing and Balancing: Buildings 1 Reroofing: Building 1

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$151,000	\$105,467	\$45,533
Construction	\$1,956,613	\$1,495,627	\$460,986
Direct Purchase	\$218,387		\$218,387
Construction Mgmt	\$263,850	\$249,338	\$14,512
Contingency	\$108,300		\$108,300
Consultants	\$2,150	\$1,794	\$356
Project Total:	\$2,700,300	\$1,852,226	\$848,074

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

PIP rubber surfacing, Basketball shade structure, Aiphone submaster station, Recorderx, (2) AC adapters & Laptops

BUDGET

\$100,000

ATHLETICS

✓ COMPLETE

SCOPE

NULL

MUSIC

✓ COMPLETE

SCOPE

372 Instruments Delivered

TECHNOLOGY

✓ COMPLETE

SCOPE

300 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Coral Cove Elementary School



Address: 5100 SW 148 AVENUE, MIRAMAR 33027
 Location Num: 2011
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$694,303
 Total Facilities Budget (Sum of Projects): \$148,000

PRIMARY RENOVATIONS P.002122 Coral Cove ES - SMART HVAC Improvements

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

Project is financially closed out and will no longer be reported on as of FY 22 Q3

PROJECT SCOPE

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$51,071	\$22,796	\$28,275
Construction Mgmt	\$11,500	\$11,500	\$0
Contingency	\$85,429		\$85,429
Project Total:	\$148,000	\$34,296	\$113,704

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

(46) LCD projectors ceiling mounted

BUDGET

\$100,000

ATHLETICS

SCOPE

COMPLETE NULL

MUSIC

SCOPE

COMPLETE 311 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 536 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Dolphin Bay Elementary School



Address: 16450 MIRAMAR PARKWAY, MIRAMAR 33027
 Location Num: 3751
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$300,718
 Total Facilities Budget (Sum of Projects):

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE	BUDGET
COMPLETE	\$100,000

DELIVERED
 Projectors, Morning Announcement Studio Equipment, Recordex, Laptops,
 New Playground Equipment Pre-K

ATHLETICS

✓ COMPLETE **SCOPE**
 NULL

MUSIC

✓ COMPLETE **SCOPE**
 655 Instruments Delivered

TECHNOLOGY

✓ COMPLETE **SCOPE**
 208 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
 An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
 An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
 A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Everglades High School



Address: 17100 SW 48 COURT, MIRAMAR 33027
 Location Num: 3731
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$7,625,580
 Total Facilities Budget (Sum of Projects): \$5,948,885

PRIMARY RENOVATIONS P.001985 Everglades HS - SMART Program Renovations

CURRENT PHASE

7-Final Completion

RISK LEVEL

No Risk

PROJECT UPDATE

This project achieved Substantial Completion (Certificate of Occupancy 110B) on 3/9/2021. Board approval of the Final Acceptance/Final Change order/ Final Retainage was on 5/18/2021. The Certificate of Final Inspection (OEF 209) form was received on 6/29/2021. The warranty walkthrough was conducted on 10/28/2021 and closeout docs were submitted on the same day. The purchase orders are in the process of being closed.

PROJECT SCOPE

Reroofing: Buildings 1, 2, & 3 HVAC Improvements: Buildings 1 (Test & Balance), 2 (Chiller Replacement, Test & Balance, Exhaust Fans, and Exhaust), and 3 (Exhaust Fans, Test & Balance, and small diameter exhaust)

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$246,836	\$246,836	\$0
Construction	\$4,102,865	\$4,102,865	\$0
Direct Purchase	\$949,247	\$949,247	\$0
Construction Mgmt	\$649,937	\$649,937	\$0
Project Total:	\$5,948,885	\$5,948,885	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Laptops, (6) Printers, Aiphone & Strike

BUDGET

\$100,000

ATHLETICS

✓ COMPLETE **SCOPE**
Weight Room

MUSIC

✓ COMPLETE **SCOPE**
327 Instruments delivered

TECHNOLOGY

✓ COMPLETE **SCOPE**
1,312 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Fairway Elementary School



Address: 7850 FAIRWAY BOULEVARD, MIRAMAR 33023
 Location Num: 1641
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$7,891,469
 Total Facilities Budget (Sum of Projects): \$7,510,900

PRIMARY RENOVATIONS P.001785 Fairway ES - GOB Renovations

CURRENT PHASE

5-Construction

RISK LEVEL

No Risk

PROJECT UPDATE

1. Final inspections for Media Center doors Inspection scheduled for 10/13/2022. 2. Installation of louver for room #516. 3. 110B has been submitted.

PROJECT SCOPE

Aluminum Covered Walkway Repairs Re-roofing to Buildings 1, 2, 3, 4, 5, 6, 7, 8, & 75 Mechanical Improvements: Buildings 1 (1 AHU), 2 (2 AHU & 10 VAV), 3 (4 AHU), 4 (1 AHU), 5 (2 AHU), 6 (1 AHU), 7 (1 AHU & 1 RTU), and 75 & 78 (2 BARD units, 2 AHU) Fire Alarm System Replacement: Campus-wide Emergency Lighting & Exit Signage Replacement: Campus-wide Building, Canopy, and Pole Lighting Replacement: Campus-wide Media Center Improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$604,124	\$550,372	\$53,752
Construction	\$5,758,146	\$5,614,050	\$144,096
FF&E and Technology	\$52,700	\$30,999	\$21,701
Direct Purchase	\$438,499	\$438,499	\$0
Construction Mgmt	\$551,960	\$425,431	\$126,529
Contingency	\$83,471		\$83,471
Consultants	\$22,000	\$14,006	\$7,994
Project Total:	\$7,510,900	\$7,073,357	\$437,543

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Color poster, Two-way radios, Projectors, Document cameras, Morning show equipment, Sound stage projector, Cafeteria sound system, microphones for the sound system, laptops, Digital marquee, Adaptors, TV installation, Desktop

BUDGET

\$100,000

ATHLETICS

✓ COMPLETE

SCOPE

NULL

MUSIC

✓ COMPLETE

SCOPE

450 Instruments delivered

TECHNOLOGY

✓ COMPLETE

SCOPE

202 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Hawkes Bluff Elementary School



Address: 5900 SW 160 AVENUE, DAVIE 33331
 Location Num: 3131
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$7,395,850
 Total Facilities Budget (Sum of Projects): \$6,852,890

PRIMARY RENOVATIONS P.001784 Hawkes Bluff ES - GOB Renovations

CURRENT PHASE

5-Construction

RISK LEVEL

No Risk

PROJECT UPDATE

HVAC Improvements: Buildings 1 (1 CU & 10 FCU), 2 (2 FCU & 2 Chillers), 3 (1 RTU, 1 AHU, 3 FCU), 4 (5 Gravity Ventilators, 9 FCU), 5 (7 Gravity Ventilators, & 12 FCU), 6 (4 Gravity Ventilators, & 7 FCU), & 8 (Wall unit) Re-roofing: Buildings 1, 2, 3, 4, 5, & 75

PROJECT SCOPE

No construction activities took place.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$573,022	\$554,509	\$18,513
Construction	\$4,515,418	\$4,441,471	\$73,947
Direct Purchase	\$902,202	\$893,505	\$8,697
Construction Mgmt	\$672,083	\$340,877	\$331,206
Contingency	\$170,165		\$170,165
Consultants	\$20,000		\$20,000
Project Total:	\$6,852,890	\$6,230,362	\$622,528

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Student chairs, LCD projector, Primary Playground Upgrades, Classroom blinds, shade structure, AC Adaptor

BUDGET

\$100,000

ATHLETICS

✓ COMPLETE

SCOPE

NULL

MUSIC

✓ COMPLETE

SCOPE

239 Instruments delivered

TECHNOLOGY

✓ COMPLETE

SCOPE

300 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Lakeside Elementary School



Address: 900 NW 136 AVENUE, PEMBROKE PINES 33028
 Location Num: 3591
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$4,891,240
 Total Facilities Budget (Sum of Projects): \$4,284,240

PRIMARY RENOVATIONS P.002070 Lakeside ES - SMART Program Renovations

CURRENT PHASE

5-Construction

RISK LEVEL

No Risk

PROJECT UPDATE

No work at this time All scopes have been completed.

PROJECT SCOPE

Electrical Improvements Exterior Lighting: Campus-wide HVAC Improvements Duck Heater, AHU Building 4, Controls: Building 17 Window-mount A/C: Building 4 Re-Roofing: Building 4, 8, 9, & 10

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$245,000	\$182,261	\$62,739
Construction	\$2,937,279	\$776,621	\$2,160,658
Direct Purchase	\$427,027	\$300,556	\$126,471
Construction Mgmt	\$456,969	\$456,969	\$0
Contingency	\$206,965		\$206,965
Consultants	\$6,000		\$6,000
Utilities	\$5,000		\$5,000
Project Total:	\$4,284,240	\$1,716,407	\$2,567,833

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Promethean boards, Stools, 10-piece portable work stations, Flexible chairs, Digital Marquee. Laptops

BUDGET

\$100,000

ATHLETICS

✓ COMPLETE SCOPE
NULL

MUSIC

✓ COMPLETE SCOPE
361 Instruments delivered

TECHNOLOGY

✓ COMPLETE SCOPE
372 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Miramar High School



Address: 3601 SW 89 AVENUE, MIRAMAR 33025
 Location Num: 1751
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$23,199,935
 Total Facilities Budget (Sum of Projects): \$21,538,560

PRIMARY RENOVATIONS P.002003 Miramar HS - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5-Construction



PROJECT UPDATE

The Fire sprinkler shop drawing was approved, the fire alarm shop drawing is still pending. The band room demolition is in process, the rough ductwork installation is 95% complete, concrete pouring was complete, and the masonry walls and framing are in progress. Campus-wide the roof work is in progress. The aviation lab renovation is in progress. Cooling towers were delivered to the site, pending ASI#5 approval for installation. The temp chiller shop drawing is in the review process.

PROJECT SCOPE

Fire Alarm System: Campus-wide, Fire Sprinklers Building 2, Re-Roofing Buildings 2, 3, 9, & 10, Rooftop Cabling Buildings 1, 2, 4, 5, 7, 8, and 14. Window replacement Building 4 & 12, Door replacement Buildings 1, 4, 9, & 12. Restroom renovations Buildings 2 & 4, Remodel of Band Room, Media Center, & Art Room Building 1. Repair of Fume Hoods Building 7. HVAC Improvements: Campus-wide. Electrical Improvements Building 7 & 8.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$854,075	\$685,470	\$168,605
Construction	\$14,547,718	\$2,304,707	\$12,243,011
FF&E and Technology	\$310,000	\$580	\$309,420
Direct Purchase	\$3,125,398	\$755,692	\$2,369,706
Construction Mgmt	\$1,941,800	\$1,941,800	\$0
Contingency	\$681,569		\$681,569
Consultants	\$55,000	\$10,721	\$44,279
Utilities	\$23,000		\$23,000
Project Total:	\$21,538,560	\$5,698,970	\$15,839,590

FLAG: SCHEDULE, Reason:Contractor Delays

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Golf cart, security cameras, scrubber machine, protective mats for gym floor, canopy fabric, auditorium painting and signage for gym & stadium, additional parking spaces

BUDGET

\$100,000

ATHLETICS

✓ COMPLETE SCOPE
Track, Weight Room

MUSIC

✓ COMPLETE SCOPE
656 Instruments delivered

TECHNOLOGY

✓ COMPLETE SCOPE
1,035 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

New Renaissance Middle School



Address: 10701 MIRAMAR BOULEVARD, MIRAMAR 33027
 Location Num: 3911
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$4,045,999
 Total Facilities Budget (Sum of Projects): \$3,554,000

PRIMARY RENOVATIONS P.002143 New Renaissance MS - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

4-Bid & Award



PROJECT UPDATE

9/7/22 Internal review meeting of GMP Negotiation meeting outcomes and Draft GMP. Attend TL, PM, Akin (Armen), and A/E. 9/9/22 TL and PM reviewed with Thornton and commented on the GMP's "Clarification, Exclusions, and comments" with CMAR for incorporation into Rev1 for the GMP. 9/13/22 Received GMP Rev 1. 9/21/22 Internal team reviewed the latest GMP and had the following Recommendations to the Program Director. 19/28/22 AECOM team met with Thornton team to clarify the difference between the Atkin Stucco and the Thornton Stucco numbers- Thornton Stucco numbers have additional project management, QA/QC, and laborers, plus the cost of the bonding agent, these represent \$1.2 mil.

PROJECT SCOPE

Exterior stucco repair - Bldg 1, 2, 3, and 4. Roof replacement - Bldg 1, 2, 3, and 4. Exterior painting - Bldg 1, 2, 3, and 4. HVAC component replacement - Bldg 1, 2, 3, and 4. HVAC test and balance - Bldg 1, 2, and 3.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$296,150	\$195,203	\$100,947
Construction	\$2,360,000	\$2,711	\$2,357,289
Construction Mgmt	\$778,250	\$748,793	\$29,457
Contingency	\$99,600		\$99,600
Consultants	\$20,000	\$1,008	\$18,992
Project Total:	\$3,554,000	\$947,715	\$2,606,285

FLAG:

No Data Available

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Aiphone and Strike, Locks replacement, Digital Marquee, Printer, Apple Chargers

BUDGET

\$100,000

IN PROGRESS

Media Furniture

ATHLETICS

✓ COMPLETE

SCOPE
NULL

MUSIC

✓ COMPLETE

SCOPE
158 Instruments Delivered

TECHNOLOGY

✓ COMPLETE

SCOPE
447 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Panther Run Elementary School



Address: 801 NW 172 AVENUE, PEMBROKE PINES 33029
 Location Num: 3571
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$3,986,929
 Total Facilities Budget (Sum of Projects): \$3,531,929

PRIMARY RENOVATIONS P.002069 Panther Run ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

6-Substantial Completion/Closeout



PROJECT UPDATE

HVAC Improvement, Controls, Chiller Pumps. Re-roofing: Buildings 1 & 3 Joint Sealant Repair and Brick Restoration

PROJECT SCOPE

The Certificate of Occupancy (form 110b) was fully executed on 6/21/2021. The project was approved by the Board during the August 2021 RSBM and The Certificate of Final Inspection (Form 209) was completed on 8/24/2021. Closeout Binders were turned over to the school on 12/15/2021 The 6-month warranty walk-through was completed on 12/15/2021. Currently, the GC is working on some warranty defects discovered during the walk-through. The final walkthrough which was scheduled for June 15th canceled due to warranty item updates. The meeting will be rescheduled after the items are complete.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$173,500	\$126,477	\$47,023
Construction	\$2,369,226	\$2,369,226	\$0
Direct Purchase	\$514,022	\$514,022	\$0
Construction Mgmt	\$391,927	\$391,927	\$0
Contingency	\$80,304		\$80,304
Consultants	\$2,950	\$2,950	\$0
Project Total:	\$3,531,929	\$3,404,602	\$127,327

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

IMPLEMENTATION

DELIVERED

Two-way radios, Aiphone, TV, ActivPanels promethean boards, Digital marquee, laptops, desktops, Recordex, TV wall mount

BUDGET

\$100,000

IN PROGRESS

Audio Visual parts, Portable PA

ATHLETICS

✓ COMPLETE SCOPE
NULL

MUSIC

✓ COMPLETE SCOPE
272 Instruments Delivered

TECHNOLOGY

✓ COMPLETE SCOPE
213 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Pembroke Lakes Elementary School



Address: 11251 TAFT STREET, PEMBROKE PINES 33026
 Location Num: 2661
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$5,236,857
 Total Facilities Budget (Sum of Projects): \$4,861,900

PRIMARY RENOVATIONS P.001842 Pembroke Lakes ES - SMART Program Renovations

CURRENT PHASE

5-Construction

RISK LEVEL



PROJECT UPDATE

Fire Alarm installation continued in Rooms 149 (Mechanical Room) and 159 (Kitchen) in preparation for the Fire Function Test. Plumbing and plumbing appurtenances installation continued in Rooms 149, 151 & 152 in preparation for achieving a Building and Plumbing Final Inspection. Electrical Equipment installation continued in Room 149 in preparation for an Electrical Final Inspection.

PROJECT SCOPE

Restroom Renovations: ADA Restrooms #151 (Female) & #152 (Male) Aluminum Walkway Repairs New Fire Alarm System (in Progress) Mechanical Improvements: Buildings 1 (10 AHU, 10 Duct heaters, 2 Gravity vents, 2 CHW circulation pumps, 1 MAU, & 1 KEF), 2 (2 Gravity Ventilators) Kitchen Work (Electrical, HVAC ductwork & Ceiling)

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$217,070	\$217,070	\$0
Construction	\$1,732,579	\$534,448	\$1,198,131
FF&E and Technology	\$69,876	\$69,875	\$1
Direct Purchase	\$166,820	\$135,565	\$31,255
Construction Mgmt	\$366,669	\$366,669	\$0
Contingency	\$95,386		\$95,386
Consultants	\$8,500		\$8,500
Project Total:	\$2,656,900	\$1,323,627	\$1,333,273

FLAG: BUDGET, Reason: Budget Adjustment

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

PRIMARY RENOVATIONS P.002779 Pembroke Lakes ES - Temporary Roofing Bldg 1 SMART Program

CURRENT PHASE

5-Construction

RISK LEVEL

No Risk

PROJECT UPDATE

Emergency Temporary Roofing for Building 1

PROJECT SCOPE

Roof is 98% completed.

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$2,205,000	\$2,151,809	\$53,191
Project Total:	\$2,205,000	\$2,151,809	\$53,191

FLAG:

No Data Available

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



- HIGH:**
An issue that can impact the project's budget and/or schedule, a resolution is being determined.
- MEDIUM:**
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.
- LOW:**
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Pembroke Lakes Elementary School



Address: 11251 TAFT STREET, PEMBROKE PINES 33026
 Location Num: 2661
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$5,236,857
 Total Facilities Budget (Sum of Projects): \$4,861,900

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE **BUDGET**
 COMPLETE \$100,000

DELIVERED
 Classroom furniture, cafeteria sound system, digital marquee, replaced keys cylinders to teacher entrance key, Document cameras, Promethean board, radio battery

ATHLETICS

✓ **SCOPE**
 COMPLETE NULL

MUSIC

✓ **SCOPE**
 COMPLETE 250 Instruments Delivered

TECHNOLOGY

✓ **SCOPE**
 COMPLETE 130 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
 An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
 An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
 A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Pines Lakes Elementary School



Address: 10300 JOHNSON STREET, PEMBROKE PINES 33026
 Location Num: 2861
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$2,920,969
 Total Facilities Budget (Sum of Projects): \$1,725,000

PRIMARY RENOVATIONS P.002004 Pines Lakes ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5-Construction



PROJECT UPDATE

The installation of the door in Building 1 has been completed. The roofing work on Building 85 is ongoing.

PROJECT SCOPE

Building 01,-New Fire Sprinkler System, New Chilled Water, and Condenser Water Pipes, New Ceiling In Administration Area and Corridors. Test & Balance Building 02-Replace Roof Shingles, Flashing. Test & Balance Building 03-Add Secondary Egress, Replace HVAC Units, Test & Balance Building 06-Relocating Power and Data For Smart Board, Test & Balance Building 07-Test and Balance Building 85-Roofing, Flashing, Drains, Window Calking. Test & Balance

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$200,495	\$128,494	\$72,001
Construction	\$1,241,105	\$1,016,149	\$224,956
FF&E and Technology	\$60,433	\$51,718	\$8,715
Construction Mgmt	\$171,112	\$171,112	\$0
Contingency	\$48,355		\$48,355
Consultants	\$3,500	\$3,000	\$500
Project Total:	\$1,725,000	\$1,370,473	\$354,527

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Office furniture, murals, monument marquee, SPE enhancements (Fencing and Gate), Window wraps, Promethean Boards

BUDGET

\$100,000

ATHLETICS

✓ **SCOPE**

COMPLETE NULL

MUSIC

✓ **SCOPE**

COMPLETE 241 Instruments Delivered

TECHNOLOGY

✓ **SCOPE**

COMPLETE 264 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Pines Middle School



Address: 200 NW DOUGLAS ROAD, PEMBROKE PINES 33024
 Location Num: 1881
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$1,163,728
 Total Facilities Budget (Sum of Projects): \$701,730

PRIMARY RENOVATIONS P.002130 Pines MS - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5-Construction

No Risk

PROJECT UPDATE

The Building Department agreed to use the flashing detail provided by Suprema. The roofing contractor mobilized and started the remaining work

PROJECT SCOPE

Installing a new roof on Building 6 including removing and reinstalling the existing mechanical equipment. Test and balance the air handling systems in Buildings 5 & 11.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$43,500	\$29,467	\$14,033
Construction	\$559,457	\$369,724	\$189,733
Direct Purchase	\$26,546		\$26,546
Construction Mgmt	\$47,362	\$47,362	\$0
Contingency	\$22,365		\$22,365
Consultants	\$2,500	\$1,701	\$799
Project Total:	\$701,730	\$448,254	\$253,476

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4				
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

IMPLEMENTATION

DELIVERED

Generator, Traffic cones, Golf carts, Micro scrubber, Signage, Athletic equipment, Morning show equipment, Chairs, Microphones, TVs, Projectors, Signage, Chair, Scores Table & Gym chairs, Tables

BUDGET

\$100,000

IN PROGRESS

Desks, ThinkStation, Desktops, Laptop wiring

ATHLETICS

COMPLETE

SCOPE
NULL

MUSIC

COMPLETE

SCOPE
124 Instruments Delivered

TECHNOLOGY

COMPLETE

SCOPE
603 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Sea Castle Elementary School



Address: 9600 MIRAMAR BOULEVARD, MIRAMAR 33025
 Location Num: 2871
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$4,767,829
 Total Facilities Budget (Sum of Projects): \$4,319,154

PRIMARY RENOVATIONS P.001632 Sea Castle ES - GOB Renovations

CURRENT PHASE

5-Construction

RISK LEVEL



PROJECT UPDATE

Campus-wide Fire Alarm device installation and inspections are on hold pending approval of Change Orders. The fire alarm change orders have been reviewed and presented. One was approved and the other requires revisions by the contractor.

PROJECT SCOPE

HVAC Improvements inclusive of (42) FCUs, (9) AHUs, and RTU replacements, Campus-wide Fire Alarm Replacement, Building Envelope Improvements inclusive of reroofing of bldg. 80 and exterior painting, ADA chair lift installation.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$287,252	\$273,155	\$14,097
Construction	\$3,100,350	\$3,043,856	\$56,494
FF&E and Technology	\$890	\$890	\$0
Direct Purchase	\$309,354	\$300,600	\$8,754
Construction Mgmt	\$438,202	\$438,202	\$0
Contingency	\$163,106		\$163,106
Consultants	\$20,000	\$6,004	\$13,996
Project Total:	\$4,319,154	\$4,062,707	\$256,447

FLAG: SCHEDULE, Reason:Owner Delays

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Furniture, office furniture, digital marquee, shade structure, science tables, projector, cafeteria sound system, laptops chargers, High Back Executive Chair

BUDGET

\$100,000

ATHLETICS

✓ COMPLETE

SCOPE
NULL

MUSIC

✓ COMPLETE

SCOPE
131 Instruments Delivered

TECHNOLOGY

✓ COMPLETE

SCOPE
420 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Silver Lakes Elementary School



Address: 2300 SW 173 AVENUE, MIRAMAR 33029
 Location Num: 3371
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$2,788,779
 Total Facilities Budget (Sum of Projects): \$2,252,383

PRIMARY RENOVATIONS P.002009 Silver Lakes ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

7-Final Completion



PROJECT UPDATE

The Certificate of Occupancy (Form 110b) was fully executed on 9/29/2020. The project went to the board during the August 17 board meeting. The Certificate of Final Completion (Form 209) was received on 8/24/2021. Closeout binders have been received and the GC has submitted its final invoice. The One-year warranty walkthrough was held on 9/13/2021. The closeout documents were delivered to the school on 9/29/2021. Final ATP for additional fees has been completed and the AE final invoice was approved on 2/24/22. The purchase order closeout memo was processed on 3/24/2022.

PROJECT SCOPE

Reroofing: Buildings 1 & 2 HVAC Improvements: Building 1: T&B, Large Diameter Exhaust

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$162,736	\$162,736	\$0
Construction	\$1,636,846	\$1,636,846	\$0
Direct Purchase	\$218,873	\$218,873	\$0
Construction Mgmt	\$233,928	\$233,928	\$0
Project Total:	\$2,252,383	\$2,252,383	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4				
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

New Pre k-2 playground with shade and PIP surfacing

BUDGET

\$100,000

IN PROGRESS

ATHLETICS

✓ COMPLETE

SCOPE

NULL

MUSIC

✓ COMPLETE

SCOPE

634 Instruments Delivered

TECHNOLOGY

✓ COMPLETE

SCOPE

260 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Silver Palms Elementary School



Address: 1209 NW 155 AVENUE, PEMBROKE PINES 33028
 Location Num: 3491
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$4,149,285
 Total Facilities Budget (Sum of Projects): \$3,616,400

PRIMARY RENOVATIONS P.002146 Silver Palms ES - SMART Program Renovations

CURRENT PHASE

8-Financial Completion

RISK LEVEL

No Risk

PROJECT UPDATE

The warranty walkthrough occurred on 8/30/2022. The AE has been asked to invoice for the 6-month walkthrough in order to keep the books up to date.

PROJECT SCOPE

Site: Cleaning and unclogging drainage of the existing aluminum walkway covers. Re-roofing: Buildings 1, 2, and 75. HVAC improvement: Buildings 1, 2, and 75. Exterior Stucco Replacement: Building 75. Exterior Painting: Building 75.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$150,000	\$114,907	\$35,093
Construction	\$2,732,457	\$2,702,382	\$30,075
Direct Purchase	\$187,866	\$187,609	\$257
Construction Mgmt	\$416,000	\$394,952	\$21,048
Contingency	\$127,077		\$127,077
Consultants	\$3,000	\$294	\$2,706
Project Total:	\$3,616,400	\$3,400,144	\$216,256

FLAG:

No Data Available

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

IMPLEMENTATION

DELIVERED

Retrofitting the existing digital marquee , school beautification; media center/ school Improvements furniture

BUDGET

\$100,000

IN PROGRESS

Shade Structure, Projectors

ATHLETICS

✓ COMPLETE **SCOPE**
NULL

MUSIC

✓ COMPLETE **SCOPE**
205 Instruments Delivered

TECHNOLOGY

✓ COMPLETE **SCOPE**
306 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Silver Shores Elementary School



Address: 1701 SW 160 AVENUE, MIRAMAR 33027
 Location Num: 3581
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$2,610,522
 Total Facilities Budget (Sum of Projects): \$2,265,560

PRIMARY RENOVATIONS P.001906 SMART Program Renovations

CURRENT PHASE

RISK LEVEL

7-Final Completion



PROJECT UPDATE

Substantial Completion was achieved on 2/5/2020. The final release and acceptance were approved during the February 2020 RSBM and the Certificate of Final Acceptance (Form 209) was fully executed on the same day. The audit of the closeout documents was conducted and the binders were submitted to the district on 8/31/2021 and to the school on 9/29/2021. The AE confirmed their Warranty Walkthrough was conducted. The purchase order memos were submitted to Capital for closeout. The project is complete.

PROJECT SCOPE

Re-roofing: Building 1 HVAC Improvements - Test & Balance: Building 1. Lightning Protection: Building 1

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$160,596	\$148,839	\$11,757
Construction	\$1,804,496	\$1,804,496	\$0
Construction Mgmt	\$249,211	\$249,211	\$0
Contingency	\$51,257		\$51,257
Project Total:	\$2,265,560	\$2,202,546	\$63,014

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Student laptops, classroom furniture, furniture for computer lab and related arts, electric strike and proximity pad, Shades & Student furniture for the media center, Computer Accessories

BUDGET

\$100,000

IN PROGRESS

Think Center

ATHLETICS

✓ COMPLETE SCOPE
NULL

MUSIC

✓ COMPLETE SCOPE
155 Instruments Delivered

TECHNOLOGY

✓ COMPLETE SCOPE
202 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Silver Trail Middle School



Address: 18300 SHERIDAN STREET, PEMBROKE PINES 33331
 Location Num: 3331
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$7,653,149
 Total Facilities Budget (Sum of Projects): \$6,808,150

PRIMARY RENOVATIONS P.001406 Silver Trail MS - GOB Renovations

CURRENT PHASE

7-Final Completion

RISK LEVEL

No Risk

PROJECT UPDATE

The project is expected to go to the October Board for a reduction in retainage from 5% - 1%. Then final release.

PROJECT SCOPE

Building Envelope Improvements inclusive of reroofing of Buildings 2 and 3, HVAC Improvements are inclusive of the replacement of heat pump AHUs, cooling towers, and exhaust fans.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$480,230	\$469,109	\$11,121
Construction	\$4,470,398	\$4,431,007	\$39,391
Direct Purchase	\$481,200	\$481,200	\$0
Construction Mgmt	\$651,456	\$651,456	\$0
Contingency	\$110,866		\$110,866
Consultants	\$9,000		\$9,000
Project Total:	\$6,203,150	\$6,032,772	\$170,378

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Silver Trail Middle School



Address: 18300 SHERIDAN STREET, PEMBROKE PINES 33331
 Location Num: 3331
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$7,653,149
 Total Facilities Budget (Sum of Projects): \$6,808,150

PRIMARY RENOVATIONS P.001650 Silver Trail MS - Roofing

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

The project has achieved Phase 8 Financial Closeout and is Closed.

PROJECT SCOPE

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$582,558	\$582,478	\$80
Contingency	\$22,442		\$22,442
Project Total:	\$605,000	\$582,478	\$22,522

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Furniture for common areas, student computers & digital marquee

BUDGET

\$100,000

IN PROGRESS

ATHLETICS

✓ **SCOPE**

COMPLETE **NULL**

MUSIC

✓ **SCOPE**
COMPLETE **83 Instruments Delivered**

TECHNOLOGY

✓ **SCOPE**
COMPLETE **547 Items Delivered**

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Sunset Lakes Elementary School



Address: 18400 SW 25 STREET, MIRAMAR 33027
 Location Num: 3661
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$3,235,007
 Total Facilities Budget (Sum of Projects): \$2,799,009

PRIMARY RENOVATIONS P.001971 Sunset Lakes ES - SMART Program Renovations

CURRENT PHASE

8-Financial Completion

RISK LEVEL

No Risk

PROJECT UPDATE

The project has achieved Phase 8 Financial Closeout and is Closed.

PROJECT SCOPE

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$91,778	\$91,778	\$0
Construction	\$1,959,145	\$1,959,145	\$0
Direct Purchase	\$452,083	\$452,083	\$0
Construction Mgmt	\$296,003	\$296,003	\$0
Project Total:	\$2,799,009	\$2,799,009	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

New PreK-2 playground, shades for 3-5 play area & fencing to separate the two play areas

BUDGET

\$100,000

IN PROGRESS

ATHLETICS

✓ COMPLETE

SCOPE NULL

MUSIC

✓ COMPLETE

SCOPE 228 Instruments Delivered

TECHNOLOGY

✓ COMPLETE

SCOPE 549 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Sunshine Elementary School



Address: 7737 W LASALLE BOULEVARD, MIRAMAR 33023
 Location Num: 1171
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$4,382,232
 Total Facilities Budget (Sum of Projects): \$3,948,448

PRIMARY RENOVATIONS P.002079 Sunshine ES - SMART Program Renovations

CURRENT PHASE

5-Construction

RISK LEVEL

No Risk

PROJECT UPDATE

NTP issued. All required submittal and any RFI in progress.

PROJECT SCOPE

Fire Alarm Panel Replacement HVAC Improvements: Buildings 1 (AHU, Controls, & Distribution System), 2 (Exhaust Fan), 4 (Backdraft Dampers)8 (Exhaust Fan), 9 (Exhaust Fans, & HVAC Controls), & 14 (Exhaust Fan). Demolish Building: Building 3 (Bid alternate 1). Roofing Roof: Building 4, 10, 11, and 13. Fire Sprinkler System: Building 4. Building Expansion Joint Replacement: Building 4.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$165,361	\$92,207	\$73,154
Construction	\$3,349,808		\$3,349,808
Construction Mgmt	\$262,490	\$262,490	\$0
Contingency	\$162,379		\$162,379
Consultants	\$8,410	\$8,409	\$1
Project Total:	\$3,948,448	\$363,106	\$3,585,342

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Poster maker, headphones, laminator, classrooms rugs, portable blowers, laptops, Earthwalk cart, staff desktop, student desktop, student chairs, shelving, bookcase, pro pencil sharpeners, Ellison machine, Recordex, Athletic Equipment, Indoor Furniture

BUDGET

\$100,000

IN PROGRESS

Projectors

ATHLETICS

✓ COMPLETE

SCOPE
NULL

MUSIC

✓ COMPLETE

SCOPE
438 Instruments Delivered

TECHNOLOGY

✓ COMPLETE

SCOPE
335 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Walter C. Young Middle School



Address: 901 NW 129 AVENUE, PEMBROKE PINES 33028
 Location Num: 3001
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$16,569,553
 Total Facilities Budget (Sum of Projects): \$15,885,560

PRIMARY RENOVATIONS P.002010 Walter C. Young MS - SMART Program Renovations

CURRENT PHASE

5-Construction

RISK LEVEL

No Risk

PROJECT UPDATE

In Building 3 painting continues. In Building 4 roofing is in progress with LWIC and base sheet completed and the interply cap sheet has started. In Building 5 the new VAVs have been installed and electrical and controls work is underway. In Building 8 the unit ventilators are installed and the soffits are being repaired.

PROJECT SCOPE

Re-roofing: Buildings 1 - 14 Window & Door Replacements: Buildings 10 & 16 HVAC Improvements: Buildings 1 - 13 Electrical Improvements (HVAC related): Buildings 1 - 13
 Painting: Buildings 1 - 3, 6 - 10, 13, 16

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$675,000	\$484,803	\$190,197
Construction	\$11,023,329	\$5,707,615	\$5,315,714
Direct Purchase	\$1,914,885	\$1,714,267	\$200,618
Construction Mgmt	\$1,548,700	\$963,825	\$584,875
Contingency	\$680,646		\$680,646
Consultants	\$25,000	\$13,285	\$11,715
Utilities	\$18,000		\$18,000
Project Total:	\$15,885,560	\$8,883,795	\$7,001,765

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Golf Cart/3 repairs, cafeteria tables, TVs for Exceptional Student Ed. Program upgrades, Printers, Facilities/Janitorial equipment, technology items, two-way radios, vertical blinds, carpet in room 925, repair dinner theater bleachers, and LCD projectors.

BUDGET

\$100,000

IN PROGRESS

Chairs

ATHLETICS

✓ COMPLETE SCOPE

NULL

MUSIC

✓ COMPLETE SCOPE

125 Instruments Delivered

TECHNOLOGY

✓ COMPLETE SCOPE

654 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

West Broward High School



Address: 500 NW 209 AVENUE, PEMBROKE PINES 33029
 Location Num: 3971
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$2,016,394
 Total Facilities Budget (Sum of Projects): \$438,000

PRIMARY RENOVATIONS P.002087 West Broward HS - SMART HVAC Improvements

CURRENT PHASE **RISK LEVEL**

9-Closed



PROJECT UPDATE

Project is financially closed out and will no longer be reported on as of FY 22 Q3

PROJECT SCOPE

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$48,725	\$15,600	\$33,125
Construction Mgmt	\$34,164	\$34,164	\$0
Contingency	\$355,111		\$355,111
Project Total:	\$438,000	\$49,764	\$388,236

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE **BUDGET**

COMPLETE \$100,000

DELIVERED

Athletic equipment, CDs/DVDs, projectors, picnic benches, Black Magic Studio system, auditorium sound system, floor mats and wall wraps

ATHLETICS

✓ COMPLETE **SCOPE**
Track, Weight Room

MUSIC

✓ COMPLETE **SCOPE**
238 Instruments Delivered

TECHNOLOGY

✓ COMPLETE **SCOPE**
773 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Whispering Pines Education Center



Address: 3609 SW 89TH AVENUE, MIRAMAR 33025
 Location Num: 1752
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$5,599,046
 Total Facilities Budget (Sum of Projects): \$4,849,580

PRIMARY RENOVATIONS P.002089 Whispering Pines Education Center - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5-Construction



PROJECT UPDATE

Roof Binder was submitted and it was rejected by Building Department, requiring a design change. A flow test was performed and submitted to Miramar City and awaiting approval for permit to be issued.

PROJECT SCOPE

Exterior Door Replacement: Building 2 Exterior Door Hardware Replacement: Buildings 1, 2 & 3 Exterior Stucco Painting: Buildings 1, 2 & 3 Exterior Stucco Repair: Buildings 1, 2 & 3 Exterior Window Replacement: Building 2 Fire Alarm System: Campus-wide Fire Sprinklers: Building 2 Fire Main for New Fire Sprinkler System HVAC Improvements: Buildings 1 & 2 Reroofing: Covered Walkway, Buildings 1, 2 & 3 Test & Balance: Buildings 1, 2 & 3 Window Replacement: Building 2

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$241,410	\$182,407	\$59,003
Construction	\$3,918,648	\$78,005	\$3,840,643
Construction Mgmt	\$464,000	\$421,690	\$42,310
Contingency	\$209,432		\$209,432
Consultants	\$10,000	\$8,441	\$1,559
Utilities	\$6,090		\$6,090
Project Total:	\$4,849,580	\$690,543	\$4,159,037

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
ACTIVE CONSTRUCTION																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE
IMPLEMENTATION

BUDGET
\$100,000
IN PROGRESS
Media Center Furniture, PIP

ATHLETICS

✓ COMPLETE **SCOPE**
NULL

MUSIC

✓ COMPLETE **SCOPE**
No Program

TECHNOLOGY

✓ COMPLETE **SCOPE**
No Items

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.
